

M3 _ M A D E

M3 Design Development Limited

Unit 1, The Old Power Station,
121 Mortlake High Street,
London, SW14 8SN

Method Statement

Project Title: **LONDON DOCK – BUILDING G**

Address: **Pennington Street, Wapping, London, E1W 2BD**

Activity: **Kitchen**

Rev no.	Issued BY	Date
00	Michele Di Nicola	05/08/2026

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 1 of 45	M 3

M3 _ M A D E

Contents

1.0	INTRODUCTION	3
2.0	PROJECT ORGANISATION FOR H & S CONTROL	4
3.0	SCOPE OF THE WORKS	4
4.0	ACCESS, EGRESS SITE WELFARE & DELIVERY PROCEDURE	5
5.0	SEQUENCE & METHOD OF THE INSTALLATION	8
6.0	WASTE CONTROL	20
7.0	COMPETENCY OF THOSE INVOLVED AND EXTERNAL FITTERS	21
8.0	PLANT & EQUIPMENT TO BE USED	22
9.0	COMMUNICATION	25
10.0	SUPERVISION	26
11.0	MONITORING OF WORK	26
12.0	TECHNICAL INFORMATION	26
13.0	3RD PARTY PROTECTION	26
14.0	PPE	26
15.0	POWER SUPPLY	27
16.0	LIGHTING	27
17.0	WORKING PLATFORMS	27
18.0	EXCAVATIONS AND TEMPORARY WORKS	28
19.0	EMERGENCY PROCEDURES	28
20.0	FIRE	28
21.0	1st AID	31
22.0	SPECIAL CONTROL MEASURES	31
23.0	APPROVAL, REVIEW and BRIEFING	31
24.0	APPENDICES	32

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 2 of 45	M 3

M3 _ M A D E


1.0 INTRODUCTION

London Dock building G is a 7 to 19-storey residential building.

The site is located in Wapping in East London in the London Borough of Tower Hamlets

the Project comprises the design, execution, completion, and commissioning of Building G comprising 364 residential apartments, car parking and associated external works, all as detailed in the supporting documents.

Address: Pennington Street, Wapping, London, E1W 2BD

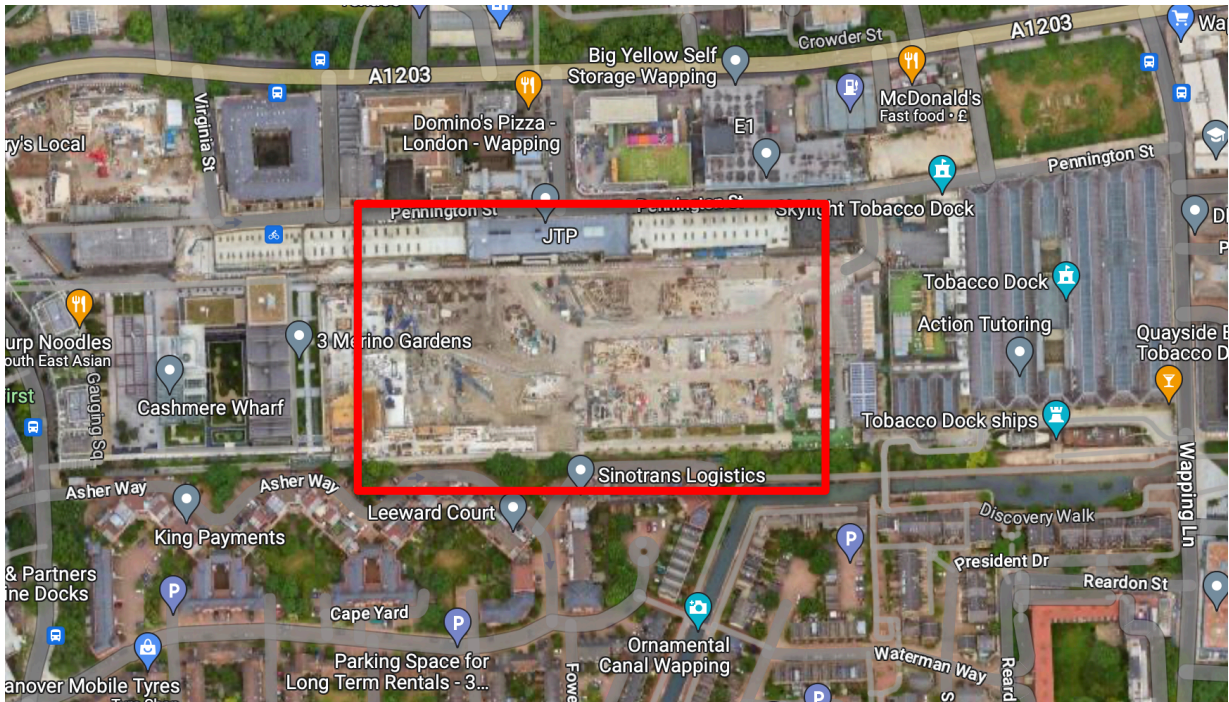

Scope:

The accommodation schedule is based on 364 Apartments with Kitchens to install.

The working hours will be:

Monday to Friday: 8am to 5pm

Saturday: 8am to 1pm

Separate permit approval will be required for any works outside agreed site hours

There are noise restriction to respect.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 3 of 45	M 3

M3 _ M A D E

2.0 PROJECT ORGANISATION FOR H & S CONTROL

The below listed operatives has the qualification requested.

Health and Safety (external Consultant):	Peter Wildi (07739612622)
Operation Director	Michele Di Nicola (+44 (0) 7585249768) Reg.no.13409586 CSCS+SMSTS
Site Manager for M3	Shaharyar Ali M. 07442 570211 - (CSCS Card no.14149051)
First aid:	Shaharyar Ali (Cert SIADS647505021997)

Legislation to follow

- Health and Safety Work Act 1974
- The Management of Health and Safety at Work Regulations 2006
- Workplace (Health, Safety and Welfare) Regulations 1992
- The Control of Asbestos Regulations 2012
- Provision and Use of Work Equipment Regulations (PUWER) 1998
- Control of Substances Hazardous to Health Regulations 2002
- The Work at Height Regulations 2005
- The Personal Protective Equipment at Work Regulations 2002
- The Manual Handling Operations Regulations 1992
- The Construction (Design and Management) Regulations 2015
- Electricity at Work Regulations 1989
- The Pressure Systems Safety Regulations 2000
- Pressure Equipment Regulations 1999 (SI 1999/2001)

The below there is the organogram of the M3 team and the qualification requested.

DESIGN MANAGEMENT	SITE OPERATION	COMMERCIAL DIRECTOR
FABIO MARINI fabio.marini@M3ltd.com	MICHELE DI NICOLA michele.dinicola@M3ltd.com	EDOARDO REGALI edoardo.regali@M3ltd.com

3.0 SCOPE OF THE WORKS

M3 scope of work is to supply and install the residential kitchens. The aim is to achieve the Practical Completion to all the private apartments

In details the scope of works is:

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 4 of 45	M 3

M3 _ M A D E

- The preparation, production and submission of design, reports, submittals, shop drawings, as-built drawings, certificates, sample details and all other documentation required to carry out the works
- To supply and install of kitchens including doors, carcasses, shelves, drawers etc.
- To template, supply and install of worktops
- To supply and install of appliances
- To supply and install of accessories
- Installation of the LED light cabling and connection to the drivers (final connections to be co-ordinated with services Trade Contractors; M3 is not connecting power to the main source).
- Installation of the taps, dry fit (connection to be co-ordinated with the services Trade Contractors; M3 is not performing any wet fit connection).

There are no specific civil works to be completed by M3 to this project.

4.0 ACCESS, EGRESS SITE WELFARE & DELIVERY PROCEDURE

The access to site will be as per the site logistics plan / drawing. This may be changed from time to time to suit the changing site activities.

All vehicles coming into the site are directed to enter the site via, Nathan Way.

All deliveries to the London Dock Block G are to be booked in on the Datascope booking system and approved by STG Logistics Manager. The delivery must be booked at least 48 hrs in advance.

M3 managers will be provided with a log in for booking deliveries. Coordination between the contractor site team, the STG project team and the individual building loading traffic management teams is vital to ensure the seamless operation of the project, leading to the harmonious integration of a site wide Traffic Management Delivery Plan.

Vehicular access onto site shall be through a designated vehicle access point that is physically segregated from the pedestrian access, with sufficient space for a vehicle to be parked off the public highway.

All access to, on & around the site will be on a shared basis with other Contractors and M3 Ltd shall coordinate his access requirements so as to cause no disruption to his own or other Contractors' activities.

- Vehicle parking restrictions: no unauthorised parking on site. STG traffic marshals are empowered to control vehicle access and egress.
- Site entrance control points and vehicle barrier types: site entrances will be signed. Barriers will be used across vehicle access gates during the day when the main gates are unlocked and open – these are to be operated by the traffic marshals and will limit unauthorised access/egress during the shift.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 5 of 45	M 3

M3 _ M A D E

The plan over indicates the site boundary, current site entrance and Exit and key on site facilities and access routes.

The Site Entrances and Exit Points are designed to give adequate vision of vehicles entering / leaving site to members of the public on foot and other road users and give adequate vision to delivery drivers.

The delivery will not be offloaded/allowed on site until a traffic marshall from the Subcontractor is present. The black hat must ensure that the delivery driver reads and signs, then complies with the rules for delivery drivers

Pedestrian access to the site will be controlled by the double Face Recognition System. Once through the system the blue route allows access/egress to the site welfare set up with changing room, hot & cold canteen and first aid room. The induction room is located in the main site office.

Access to site is from Pennington St then the site entrance is situated on the right-hand side (see below the red arrow).



All visitors, operatives and staff will sign in. Security turnstiles will be used to control access to site.

All visitors, operatives and staff must attend the Site Safety Induction, after which a security pass shall be issued permitting access onto the site.

a) All personnel must check in when entering the site at the security office.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 6 of 45	M 3

M3 _ M A D E

b) Pedestrian access to the site will be controlled by the use of electronic security turnstiles.

c) As a precautionary measure, persons entering and leaving the site may be subject to random bag searches.

d) Any person failing to comply with the site rules or to act in a responsible manner shall be denied any further access to the site.

e) All Contractor's managers and operatives are to hold CSCS accreditation at the requisite level required of each person to carry out their works. Non CSCS holders will not be permitted to work on the site

f) The Contractor should note the nature of the site area and familiarise themselves with the adjacent roadways, access and egress routes to ascertain the most serviceable route.

Site inductions will include current logistics, safety issues, safety awareness, site management personnel, and the welfare amenities.

In order to be successfully inducted and consequently be permitted to work on site each operative will have to meet the following requirements:

- Have the correct 5 point PPE.
- Hold a valid CSCS card which is relevant to the role they will be undertaking on site
- Have evidence they have had their RAMS briefing from their supervisor and that they have clearly understood these RAMS
- Clearly state where they hold any other skills cards or qualification relevant to their role including SMSTS, SSSTS (for site managers and site supervisors), CPCS (for plant operators), etc.
- Have a second means of identification.

They will be expected to present any cards, identification, etc. at the induction.

Security passes will only be issued following successful inductions and presentation of certification and training cards

Delivery vehicles will be admitted only when M3 manager will be in attendance;

All vehicles will be booked in, in advance in order to avoid congestion of the site entrance and surrounding street.

MANDATORY DELIVERY DRIVER RULES:

1. Site speed limit of **5 mph**, or lower where posted. This is walking speed.
2. No reversing on site without a banksman
3. Mandatory PPE – Hard Hat, Hi-Vi, Safety Boots, Eye Protection and Gloves must be worn outside of cab. No Shorts allowed outside cab.
4. Only park where instructed. Do not stop on site roads.
5. Do not use mobile phones when driving.
6. Obey all road traffic signage.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 7 of 45	M 3

M3 _ M A D E

7. Wear seatbelts at all times whilst moving.
8. You must have appropriate training for all equipment and plant that you will be operating.
9. All drivers are responsible for checking ground conditions before exiting cab. Climb out of cab carefully using steps and hand holds where provided.
10. No animals, children or unauthorised passengers permitted onto site.
11. No Drugs & Alcohol permitted. Do not come onto site under the influence of drugs or alcohol.
12. No smoking, eating or drinking on site or in vehicle cabs.
13. Keys must not be left in unattended vehicles.
14. Do not climb onto the back of your vehicle under any circumstances unless:
 - Fall Prevention (Handrails, harness system or similar) is fitted
 - Good access is provided (ladder, steps etc)
 - You have been briefed on the safe system of work
 - You are competent (trained and experienced) to do so
15. Take care as you leave site - be careful for pedestrians, cyclists and other road users. Do not speed, be considerate and follow the correct route.
16. Failure to comply with these rules will result in you being asked to leave site, regardless of whether you have unloaded or not.

5.0 SEQUENCE & METHOD OF THE INSTALLATION

The proposed sequence of works is indicated upon the installation programme, but it is indicative and can be changed according with the site condition.

M3 usually use TOOL BOX to stock the tools or it could be necessary to have a small room to leave tools and materials; it could be necessary an area to stock joinery (pre agreed location) if needed and a room on site dedicated to do the cut.

The installation sequence will be the same for all the units and it will be as follow:

1. Materials will be delivered to site on a previously agreed date and time.
2. Materials will be unloaded with a forklift (kitchens) or by hand from the rear or the side of the vehicle only (please see the Materials Journey Plan for more details). M3 could use a Lorry Pod as a barrier. The pallets/materials will be moved in a storage compound on site. The vertical distribution will be done with crane/hoist/internal lift that the main contractor will provide on-site. M3 operatives will move the material until the hoist/lift, which will be used to distribute the products onto the right levels. Once the goods will be lifted to the relevant floor, the M3 operatives can distribute the goods in the correct plot to the point of installation (Appendix 2 - Manual Handling Assessment" attached). M3 will move the goods by hand to the plot or using mechanical aids. The materials have to be moved safely

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 8 of 45	M 3

M3 _ MADE

according with the H&S regulation (Use mechanical aids to move loads if possible; adopt the correct position when lifting; bend your knees and keep a straight back; make a base with your feet, close to the load, wear gloves; ask for assistance when lifting awkwardly shaped loads; tell your supervisor if you suffer from back pain).
Please check the “Weight limit table” at the end of the paragraph.


The Lorrypod gives the operative an easy and safer way to load and unload cargo when working on the beds of vehicles. This vehicle access podium has a self closing gate and enclosed platform for extra security when working at height.

With the Lorrypod in place the operative will have an enclosed platform for moving loads on the back of vehicles.

The Lorrypod is manufactured under ISO:9001:2008



Specific information of the Lorry pod:

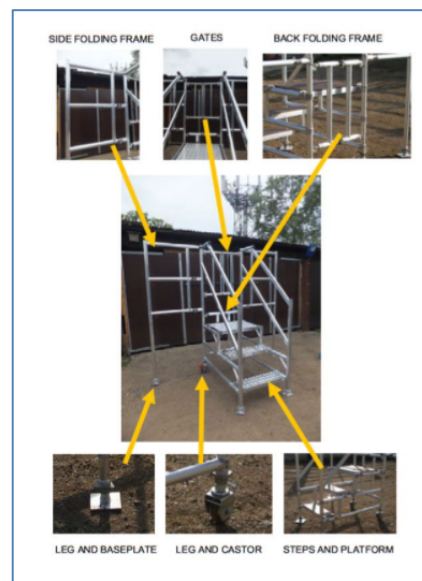

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 9 of 45	M 3

M3 _ M A D E

Specification:

Ladder Material	Aluminium
Max Working Height (metres)	1.2m or 1.5m (Trailer Height)
Platform Height	0.9m or 1.2 m
Platform Size	600 x 850 mm
Open Dimensions	Width When Erected 2.5 m
More Specifications	Safe Working Load: 150 kg

Appliances deliveries: M3 may need to use skate with castors (please see picture below) / Dolly to move and distribute to located apartments. The appliances will be delivered on Lorry with tail lift and barriers (please see the Materials Journey Plan for more details).



3. Before Installation: M3 will check that the area is clear from all debris and opening sizes are as per latest issued drawings and within any agreed tolerances.
4. Subject to the correct checking of the above point (3) M3 will commence the installation. Furniture goods will be removed from packaging as required. Goods will be installed in accordance with the agreed M3 project drawings. During the installation all the tools must be used by competent and trained workers, always in a safe way and according to manufacturer's instruction; If a datum level is provided goods will be installed to an agreed datum level and co-ordinated with other trades.
5. During the installation M3 may be required to cut some elements of the joinery using a chop saw and elements of joinery may be required to be fixed in place using battery powered handheld power tools. Please see specific risk assessment for these items.
6. M3 is responsible also for partial electrical connections (connection of the drivers to the kitchen LED but not the connection to main power) and partial plumbing connections (traps installations into the sink, no wet connection are performed by M3) to do in coordination also with services Trade Contractors.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 10 of 45	M 3

M3 _ M A D E

7. M3 is responsible for continually clearing up; during the works, at the end of each shift and at the end of the day and will keep all work areas and storage areas neat, tidy and well organised
8. On sectional completion of the works M3 will protect the installation, subject to agreement with the main contractor and site conditions.

KITCHENS GENERAL INSTALLATION SEQUENCE

The indicative sequence for the installation could be:

In general, the good practices before to start the Kitchen installation should be that:

1. To avoid dampness to the units, window glazing must be installed before commencing the installation.
2. Floor must be completed and fully protected to avoid damages from heavy appliances such as fridge & freezer (2nd fix). Floor must be levelled to avoid misalignment or gap between the unit and finished floor.
3. Ceiling should be painted
4. Wall must be vertical, plastered and painted. Concealed M&E services must be clearly marked to avoid damage to these services during drilling of holes for wall plugs which are used to secure the top cabinet to the wall
5. Pressure test on gas and water pipes running behind the cabinets must be successfully completed

M3 will check the site measurement against approved shop drawings.

M3 will check that the plaster work and possibly reinforcement in all areas are solid and secure.

M3 will check that all the 1st fix electrical work to include any new positions for washers, dryers, dishwasher, fridge freezer, under unit lights, plinth lights and hood/extractor fan are completed and in the correct position

M3 will check that 1st fix plumbing work are done making sure supply and waste flows to and from the new appliances are in the correct position.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 11 of 45	M 3

M3 _ M A D E

M3 can then start with the 1st fix with the following activities (1st visit): base unit installation, then wall units making sure the height between units is correct to match any tall cupboards and the approved shop drawings. All the kitchen cabinets must be secured together with adequate joinery screws and approved wall plugs. The cabinets and bases must be fixed in level and aligned and finally secured.

M3 will then arrange the 2nd visit for the Worktops and splashback to be templated.

M3 will then arrange the 3rd visit for the Worktops/Splashback and Sinks to be installed.

OTHERS will install the floor

OTHERS will complete the decoration

OTHERS will complete the LIVE TESTING

M3 will then arrange the 5th visit AFTER LIVE TESTING to complete the 2nd fix of the kitchen that includes all appliances (Incl. hardwiring by others) and accessories installations.

Interfacing activities include:

- 1) co-ordination with the electrical contractor with regards to socket positions, power for appliances that will be installed, and also the powering of LED light strips situated in the bottom of the high level units. M3 drawings to be followed by other trades to ensure the sockets and cables are in the correct location. No electrical connection to main power will be done by M3 Operatives.
- 2) The plumbing contractor will provide the waste and water supply for the installation of the sink and also for dishwashers that will be installed. All final electrical and plumbing connections will be carried out by others. M3 drawings to be followed by other trades to ensure the pipes are in the correct location. No wet-fit connection will be performed by M3 Operatives.

STG confirmed that they want the kitchen to be installed prior the timber floor.

PROTECTION:

Post-installation, the works will be protected with fire-retardant Correx (Proplex FR 3mm – sheets 1.2m – 2.4 m).

- Kitchens: Every door will be protected singularly.
- Worktop: Correx to cover all the surface and the edges
- Appliances: hob, oven and microwave will be protected as glass exposed

M3 to supply QI check sheet in every completed stage of installation.

Please see below the table with the WEIGHT LIMIT LEVEL:

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 12 of 45	M 3

Item	PART	MODEL	H (mm)	L (mm)	P (mm)	WEIGHT	No. of Operatives
Lh corner sink unit W992, 1 door W600 + 1 fixed front, internal panel W392	Kitchen	N/A	720	992	570	25kg< box < 50 kg	2no. Operatives
Rh base unit W551 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	551	570	25kg< box < 50 kg	2no. Operatives
Lh base unit W600 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	600	570	25kg< box < 50 kg	2no. Operatives
Rh hob base unit W600 1 TTO door + 1 drawer, 1 shelf (MIELE KM7201FR)	Kitchen	N/A	720	600	570	25kg< box < 50 kg	2no. Operatives
Package 1: Rh+ Lh sides refrigerator tall unit (Miele KDN 7724E)	Kitchen	N/A	2150	548	36	25kg< box < 50 kg	2no. Operatives
Package 2: Top + bottom tall unit (Miele KDN 7724E)	Kitchen	N/A	563,5	547,5	36	box < 5 kg	1no. Operative
Package 3: Back panel refrigerator tall unit H312 (Miele KDN 7724E)	Kitchen	N/A	312	578	8	box < 5 kg	1no. Operative
Package 4: Rh lower H750 door refrigerator tall unit (Miele KDN 7724E)	Kitchen	N/A	747	597	19	25kg< box < 50 kg	2no. Operatives
Package 5: Rh upper H1400 door refrigerator tall unit (Miele KDN 7724E)	Kitchen	N/A	1396	597	19	25kg< box < 50 kg	2no. Operatives
Package 6: Hardware	Kitchen	N/A	600	600	200	box < 5 kg	1no. Operative
Lh micro+oven tall unit W600 H2150, 1 lower door + 1 internal basket + 1 internal drawer, 1 upper TTO door, 1 shelf (Miele M2234SC + H2851B)	Kitchen	N/A	2150	600	570	Box > 50 kg	>3no. operatives, only if no mechanical means available
Rh hood wall unit W600, 1 overhanging TTO door, 1 shelf (ELICA SLEEK-60)	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W355, 1 overhanging door, 2 shelves	Kitchen	N/A	850	355	353	25kg< box < 50 kg	2no. Operatives
Lh wall unit W355, 1 overhanging door, 2 shelves	Kitchen	N/A	850	355	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W404, 1 overhanging door, 2 shelves	Kitchen	N/A	850	404	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W551, 1 overhanging door, 2 shelves	Kitchen	N/A	850	551	353	25kg< box < 50 kg	2no. Operatives
Lh wall unit W600, 1 overhanging door, 2 shelves	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Lh corner wall unit W502, 1 overhanging door W257 + 1 extra front panel W100, 2 shelves internal panel W197	Kitchen	N/A	850	502	353	25kg< box < 50 kg	2no. Operatives
Wall unit filler W20, 1 overhanging front, 1 side, 1 bottom	Kitchen	N/A	850	200	353	box < 5 kg	1no. Operative
Wall unit side panel H850 W353	Kitchen	N/A	850	353	25	box < 5 kg	1no. Operative
Dishwasher door W600 (Miele G5150 Vi)	Kitchen	N/A	717	597	19	5kg< box < 25 kg	1no. operative
Base side panel H870 W630 with grooves	Kitchen	N/A	870	630	25	box < 5 kg	1no. Operative
Tall side panel W65 H230	Kitchen	N/A	2300	650	25	5kg< box < 25 kg	1no. Operative
END tall side panel W65 H230 with grooves	Kitchen	N/A	2300	650	25	5kg< box < 25 kg	1no. Operative
Plinth H150 W2800	Kitchen	N/A	145	2800	19	box < 5 kg	1no. Operative
Base filler W250, 1 front W250 with 9 grooves + 1 fixed front, 1 side	Kitchen	N/A	720	250	150	box < 5 kg	1no. Operative
Lower filler for corner base W100 with 2 grooves	Kitchen	N/A	592	100	19	box < 5 kg	1no. Operative
BSG W250, 1 front W250 with 11 grooves + 1 depth side	Kitchen	N/A	870	250	570	5kg< box < 25 kg	1no. Operative
Underwall unit panel W1200 with led groove for SFRESE LED	Kitchen	N/A	1200	300	22	box < 5 kg	1no. Operative

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 13 of 45	M 3

M3 _ MADE

Underwall unit panel W1400 with led groove for SFRESE LED	Kitchen	N/A	1400	300	22	box < 5 kg	1no. Operative
Underwall unit Lh corner panel W2400 with led groove for SFRESE LED	Kitchen	N/A	2400	300	22	box < 5 kg	1no. Operative
Underwall unit panel W496 for hood without led groove - REAR	Kitchen	N/A	496	33	22	box < 5 kg	1no. Operative
Underwall unit panel W600 for hood without led groove - FRONT	Kitchen	N/A	600	30	22	box < 5 kg	1no. Operative
Lh corner metal frame W602 H1400, with panel W552 H800	Kitchen	N/A	1400	602	12	box < 5 kg	1no. Operative
Metal shelf W552 w/ Rh cut out plug	Kitchen	N/A	150	552	150	box < 5 kg	1no. Operative
Metal shelf W552	Kitchen	N/A	150	552	150	box < 5 kg	1no. Operative
Wall unit hanger bar	Kitchen	N/A	53	2000	6	box < 5 kg	1no. Operative
Metal profile W1200	Kitchen	N/A	20	1200	2	box < 5 kg	1no. Operative
Alluminium dishwasher rail W60	Kitchen	N/A	N/A	N/A	N/A	< 1 kg	1no. Operative
LED profile SFRESE W1200, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	1200		22	< 1 kg	1no. Operative
LED profile SFRESE W1400, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	1400		22	< 1 kg	1no. Operative
LED profile SFRESE W2400, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	2400		22	< 1 kg	1no. Operative
Rh sink base W600, 1 TTO door + 1 fixed front	Kitchen	N/A	720	600	588	25kg< box < 50 kg	2no. Operatives
Rh base unit W453 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	453	570	25kg< box < 50 kg	2no. Operatives
Lh corner unit W747, 1 TTO door + 1 fixed front W355, 1 shelf, internal panel W392	Kitchen	N/A	720	747	570	25kg< box < 50 kg	2no. Operatives
Oven base W60, 1 upper drawer (Zanussi ZOPNX6K2) (Miele H2851B)	Kitchen	N/A	742	600	570	25kg< box < 50 kg	2no. Operatives
Lh Microwave wall unit W600 1 TTO door, 1 lower front, 1 shelf (Miele M2234 SC)	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Lh hood wall unit W600, 1 overhanging TTO door, 1 shelf (ELICA SLEEK-60)	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W306, 1 overhanging door, 2 shelves	Kitchen	N/A	850	306	353	25kg< box < 50 kg	2no. Operatives
Lh wall unit W453, 1 overhanging door, 2 shelves	Kitchen	N/A	850	453	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W502, 1 overhanging door, 2 shelves	Kitchen	N/A	850	502	353	25kg< box < 50 kg	2no. Operatives
Lh wall unit W502, 1 overhanging door, 2 shelves	Kitchen	N/A	850	502	353	25kg< box < 50 kg	2no. Operatives
Dishwasher door W453 (Miele G5690 SCVi)	Kitchen	N/A	717	450	19	25kg< box < 50 kg	2no. Operatives
Lh refrigerator door W600 (Miele K31242UiF)	Kitchen	N/A	717	597	19	25kg< box < 50 kg	2no. Operatives

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 14 of 45	M 3

M3 _ MADE

Base filler W150, 1 front W150 with 4 grooves + 1 fixed front, 1 side	Kitchen	N/A	720	150	150	box < 5 kg	1no. Operative
Lower filler for corner base W150 with 4 grooves	Kitchen	N/A	592	150	19	box < 5 kg	1no. Operative
Underwall unit panel W700 with led groove for SFRESE LED	Kitchen	N/A	700	300	22	box < 5 kg	1no. Operative
Underwall unit Rh corner panel W1350 with led groove for SFRESE LED	Kitchen	N/A	1350	300	22	box < 5 kg	1no. Operative
Rh corner metal frame W725 H1400, with panel W675 H800	Kitchen	N/A	1400	725	12	box < 5 kg	1no. Operative
Metal shelf W675 w/ Lh cut out plug	Kitchen	N/A	150	675	150	box < 5 kg	1no. Operative
Metal shelf W675	Kitchen	N/A	150	675	150	box < 5 kg	1no. Operative
Metal profile W600	Kitchen	N/A	20	600	2	box < 5 kg	1no. Operative
Alluminium dishwasher rail W45,3	Kitchen	N/A	N/A	N/A	N/A	< 1 kg	1no. Operative
LED profile SFRESE W700, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	700		22	< 1 kg	1no. Operative
LED profile SFRESE W1350, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	1350		22	< 1 kg	1no. Operative
Lh corner unit W747, 1 TTO door + 1 fixed front W453, 1 shelf, internal panel W293	Kitchen	N/A	720	747	570	25kg< box < 50 kg	2no. Operatives
Package 1: Rh drill for hinge + Lh sides refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	2150	548	36	5kg< box < 25 kg	2no. Operatives
Package 3: Back panel refrigerator tall unit H302 (Zanussi ZNLN18FS1)	Kitchen	N/A	302	578	8	box < 5 kg	1no. Operative
Package 4: Rh lower H760 door refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	757	597	19	25kg< box < 50 kg	2no. Operatives
Package 5: Rh upper H1390 door refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	1386	597	19	25kg< box < 50 kg	2no. Operatives
Lh wall unit W306, 1 overhanging door, 2 shelves	Kitchen	N/A	850	306	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W453, 1 overhanging door, 2 shelves	Kitchen	N/A	850	453	353	25kg< box < 50 kg	2no. Operatives
Rh wall unit W600, 1 overhanging door, 2 shelves	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Rh corner wall unit W600, 1 overhanging door W355 + 1 extra front panel W100, 2 shelves internal panel W197	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Base short side panel H870 W150	Kitchen	N/A	870	150	25	box < 5 kg	1no. Operative
Tall short side panel W15 H230	Kitchen	N/A	2300	150	25	5kg< box < 25 kg	1no. Operative
Base filler W150, 1 front W150 with 6 grooves + 1 fixed front, 1 side	Kitchen	N/A	720	150	150	box < 5 kg	1no. Operative
Underwall unit Rh corner panel W2400 with led groove for SFRESE LED	Kitchen	N/A	2400	300	22	box < 5 kg	1no. Operative

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 15 of 45	M 3

M3 _ MADE

Rh corner sink base W992, 1 TTO door W600 + 1 fixed front W306, internal panel W392	Kitchen	N/A	720	992	588	25kg< box < 50 kg	2no. Operatives
Lh hob base unit W600 1 TTO door + 1 drawer, 1 shelf (MIELE KM7201FR)	Kitchen	N/A	720	600	570	25kg< box < 50 kg	2no. Operatives
Rh corner unit W894,1 TTO door + 1 fixed front W502, 1 shelf, internal panel W392	Kitchen	N/A	720	894	570	25kg< box < 50 kg	2no. Operatives
Lh wall unit W404, 1 overhanging door, 2 shelves	Kitchen	N/A	850	404	353	25kg< box < 50 kg	2no. Operatives
Lh corner wall unit W600, 1 overhanging door W355 + 1 extra front panel W100, 2 shelves internal panel W197	Kitchen	N/A	850	600	353	25kg< box < 50 kg	2no. Operatives
Base side panel H870 W956 with grooves	Kitchen	N/A	870	956	25	box < 5 kg	1no. Operative
BSG W100, 1 front W100 with 2 grooves + 1 depth side	Kitchen	N/A	870	100	570	5kg< box < 25 kg	1no. Operative
Underwall unit Lh corner panel W1350 with led groove for SFRESE LED	Kitchen	N/A	1350	300	22	box < 5 kg	1no. Operative
Lh base unit W306 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	306	570	25kg< box < 50 kg	2no. Operatives
Lh base unit W404 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	404	570	25kg< box < 50 kg	2no. Operatives
Rh corner unit W551,1 TTO door + 1 fixed front W257, 1 shelf, internal panel W293	Kitchen	N/A	720	551	570	25kg< box < 50 kg	2no. Operatives
Lh wall unit W551, 1 overhanging door, 2 shelves	Kitchen	N/A	850	551	353	25kg< box < 50 kg	2no. Operatives
Wall unit filler W211, 1 overhanging framed front, 1 side, 1 bottom	Kitchen	N/A	850	211	353	box < 5 kg	1no. Operative
Back tall side panel W59,7 H230 with grooves	Kitchen	N/A	2300	597	25	5kg< box < 25 kg	1no. Operative
Back island panel W1470 with grooves	Kitchen	N/A	870	1470	25	25kg< box < 50 kg	2no. Operatives
BSG W110, 1 front W110 with grooves + 2 depth sides	Kitchen	N/A	870	110	570	5kg< box < 25 kg	1no. Operative
Underwall unit Rh corner panel W800 with led groove for SFRESE LED	Kitchen	N/A	800	300	22	box < 5 kg	1no. Operative
Lh corner metal frame W655 H1400, with panel W605 H800	Kitchen	N/A	1400	655	12	box < 5 kg	1no. Operative
Metal shelf W605 w/ Lh cut out plug	Kitchen	N/A	150	605	150	box < 5 kg	1no. Operative
Metal shelf W605	Kitchen	N/A	150	605	150	box < 5 kg	1no. Operative
LED profile SFRESE W800, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	700		22	< 1 kg	1no. Operative
Rh base unit W551 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	551	570	25kg< box < 50 kg	2no. Operatives
Rh wall unit W551, 1 overhanging door, 2 shelves	Kitchen	N/A	850	551	353	25kg< box < 50 kg	2no. Operatives
Rh corner sink base W992, 1 TTO door W600 + 1 fixed front W306, internal panel W392	Kitchen	N/A	720	992	588	25kg< box < 50 kg	2no. Operatives
Rh corner unit W894,1 TTO door + 1 fixed front W502, 1 shelf, internal panel W392	Kitchen	N/A	720	894	570	25kg< box < 50 kg	2no. Operatives
Lh wall unit W404, 1 overhanging door, 2 shelves	Kitchen	N/A	850	404	353	25kg< box < 50 kg	2no. Operatives
Base short side panel island H870 W325	Kitchen	N/A	870	325	25	box < 5 kg	1no. Operative

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 16 of 45	M 3

M3 _ MADE

Base filler W250, 1 front W250 with 10 grooves + 1 fixed front, 1 side	Kitchen	N/A	720	250	150	box < 5 kg	1no. Operative
Underwall unit Lh corner panel W1350 with led groove for SFRESE LED	Kitchen	N/A	1350	300	22	box < 5 kg	1no. Operative
Lh base unit W404 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	404	570	25kg< box < 50 kg	2no. Operatives
Rh corner unit W551,1 TTO door + 1 fixed front W257, 1 shelf, internal panel W293	Kitchen	N/A	720	551	570	25kg< box < 50 kg	2no. Operatives
Lh wall unit W551, 1 overhanging door, 2 shelves	Kitchen	N/A	850	551	353	25kg< box < 50 kg	2no. Operatives
BSG W150, 1 front W200 with 5 grooves + 1 depth side	Kitchen	N/A	870	150	570	5kg< box < 25 kg	1no. Operative
Lh base unit W355 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	355	570	25kg< box < 50 kg	2no. Operatives
Rh base unit W600 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	600	570	25kg< box < 50 kg	2no. Operatives
Rh corner unit W747,1 TTO door + 1 fixed front W355, 1 shelf, internal panel W392	Kitchen	N/A	720	747	570	25kg< box < 50 kg	2no. Operatives
Package 4: Lh lower H760 door refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	757	597	19	25kg< box < 50 kg	2no. Operatives
Package 5: Lh upper H1390 door refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	1386	597	19	25kg< box < 50 kg	2no. Operatives
Lh corner wall unit W551, 1 overhanging door W306 + 1 extra front panel W100, 2 shelves internal panel W197	Kitchen	N/A	850	551	353	25kg< box < 50 kg	2no. Operatives
Rh corner metal frame W602 H850, with panel W552 H800	Kitchen	N/A	850	602	12	box < 5 kg	1no. Operative
Metal shelf W552 w/ Lh cut out plug	Kitchen	N/A	150	552	150	box < 5 kg	1no. Operative
Led driver 60W Uk plug for SFRESE led	Kitchen	N/A				< 1 kg	1no. Operative
Lh sink base W600, 1 TTO door + 1 fixed front	Kitchen	N/A	720	600	588	25kg< box < 50 kg	2no. Operatives
Rh base unit W404 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	404	570	25kg< box < 50 kg	2no. Operatives
Rh corner unit W992,1 TTO door + 1 fixed front W600, 1 shelf, internal panel W392	Kitchen	N/A	720	992	570	25kg< box < 50 kg	2no. Operatives
Underwall unit panel W2100 with led groove for SFRESE LED	Kitchen	N/A	2100	300	22	box < 5 kg	1no. Operative
LED profile SFRESE W2100, 2700K disassembled (Aluminium LED profile SFRESE+Strip LED 2700K+led wire 2m)	Kitchen	N/A	2100		22	< 1 kg	1no. Operative
Lh base unit W355 1 TTO door + 1 drawer, 1 shelf	Kitchen	N/A	720	355	570	25kg< box < 50 kg	2no. Operatives
Rh corner unit W747,1 TTO door + 1 fixed front W355, 1 shelf, internal panel W392	Kitchen	N/A	720	747	570	25kg< box < 50 kg	2no. Operatives
Package 1: Lh drill for hinge + Rh sides refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	2150	548	36	5kg< box < 25 kg	2no. Operatives
Package 4: Lh lower H760 door refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	757	597	19	25kg< box < 50 kg	2no. Operatives
Package 5: Lh upper H1390 door refrigerator tall unit (Zanussi ZNLN18FS1)	Kitchen	N/A	1386	597	19	25kg< box < 50 kg	2no. Operatives

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 17 of 45	M 3


M3 _ MADE

Lh corner unit W894, 1 TTO door + 1 fixed front W600, 1 shelf, internal panel W293 Lh side with cut out side	Kitchen	N/A	720	894	570	25kg< box < 50 kg	2no. Operatives
Package 5: Lh upper H1400 door refrigerator tall unit (Miele KDN 7724E)	Kitchen	N/A	1396	597	19	25kg< box < 50 kg	2no. Operatives
Rh micro+oven tall unit W600 H2150, 1 lower door + 1 internal basket + 1 internal drawer, 1 upper TTO door, 1 shelf (Miele M2234SC + H2851B)	Kitchen	N/A	2150	600	570	Box > 50 kg	>3no. operatives, only if no mechanical means available
Lh wall unit W453, 1 overhanging door, 2 shelves	Kitchen	N/A	850	453	353	25kg< box < 50 kg	2no. Operatives
Lh corner unit W894, 1 TTO door + 1 fixed front W502, 1 shelf, internal panel W392 Lh side with cut out side	Kitchen	N/A	720	894	570	25kg< box < 50 kg	2no. Operatives
Package 4: Lh lower H750 door refrigerator tall unit (Miele KDN 7724E)	Kitchen	N/A	747	597	19	25kg< box < 50 kg	2no. Operatives
Package 5: Lh upper H1400 door refrigerator tall unit (Miele KDN 7724E)	Kitchen	N/A	1396	597	19	25kg< box < 50 kg	2no. Operatives
Lh wall unit W300, 1 overhanging door, 2 shelves	Kitchen	N/A	850	300	353	25kg< box < 50 kg	2no. Operatives
Rh corner unit W894, 1 TTO door + 1 fixed front W502, 1 shelf, internal panel W392 Rh side with cut out side	Kitchen	N/A	720	894	570	25kg< box < 50 kg	2no. Operatives
Rh wall unit W300, 1 overhanging door, 2 shelves	Kitchen	N/A	850	300	353	25kg< box < 50 kg	2no. Operatives
Single Bowl Stainless Steel Inset with Drainer	Sink	AGX 611-78				box < 5 kg	1no. Operative
Maris single Bowl Undermounted	Sink	135.0666.807				box < 5 kg	1no. Operative
Maris 1.5 Bowl Undermounted (HANDED)	Sink	135.0666.839				box < 5 kg	1no. Operative
Elements Mono Sink Mixer Deck Mounted Black	Tap	CUC-1063-BLK				box < 5 kg	1no. Operative
Bahr Mono mixer single lever SS	Tap	CUC-1008-S/S				box < 5 kg	1no. Operative
30L 2 Compartment Bin	Bin	757621-85				box < 5 kg	1no. Operative
Single Oven	Oven	ZOPNX6K2 (or similar)	589	594	568	30 kg	2no. operative with mechanical help
Single Oven	Oven	H 2851 B (or similar)	560/568	590/595	550	42kg	2no. operative with mechanical help
Single Oven	Oven	H 7464 BP -Vline - Obs Blk (or similar)	595	596	569	47 kg	2no. operative with mechanical help
Integrated Microwave	MW	M 2234 SC - Obs Blk (or similar)	595	372	310	14.40 kg	1no. Operative
Integrated Microwave	MW	H 7440 BM -Vline - Obs Blk (or similar)	595	456	569	36 kg	2no. operative with mechanical help
60CM Electric Hob	Hob	ZHRN643K (or similar)	38	560	490	6kg	1no. Operative
2 Zone Induction Hob	Hob	CS 7612 FL (or similar)	51	378	520	7kg	1no. Operative
45cm Integrated Dishwasher	Dish washer	G5690 SC Vi (or similar)	448	845	600	40.80 kg	2no. operative with mechanical help
60CM Induction Hob	Hob	KM 7464 FL (or similar)	51	620	520	11 kg	1no. Operative
Fixed Canopy Extractor	Extractor	SLEEK-60 (or similar)	300	500	300	6kg	1no. Operative
Ceiling Extractor	Extractor	Highlight GLS White Glass H16 (or similar)	570	1000	300	21/27 kg	1no. Operative
Integrated Fridge Freezer	FF	ZNLN18FS1 (or similar)	1770	546	549	56 kg	2no. operative with mechanical help
Integrated Undercounter Fridge	Fridge	K 31242 Uif (or similar)	818	552	597	35.5 kg	2no. operative with mechanical help

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 18 of 45	M 3

M3 _ MADE

Integrated Fridge Freezer	FF	KDN 7724 E (or similar)	1772	541	548	54.80 kg	2no. operative with mechanical help
30cm Wine Cooler	Wine Cooler	WI3126 + HANDLE7BK (or similar)	820	295	573	31 kg	2no. operative with mechanical help
60cm Wine Cooler	Wine Cooler	WI6143 + HANDLE7BK (or similar)	820	595	573	50 kg	2no. operative with mechanical help
60cm Integrated Dishwasher	DW	G 5150 VI (or similar)	805	598	550	50.50 kg	2no. operative with mechanical help
Freestanding Washer Dryer	WD	WNA134U8GB (or similar)	850	600	400/700	70.93 kg	2no. operative with mechanical help

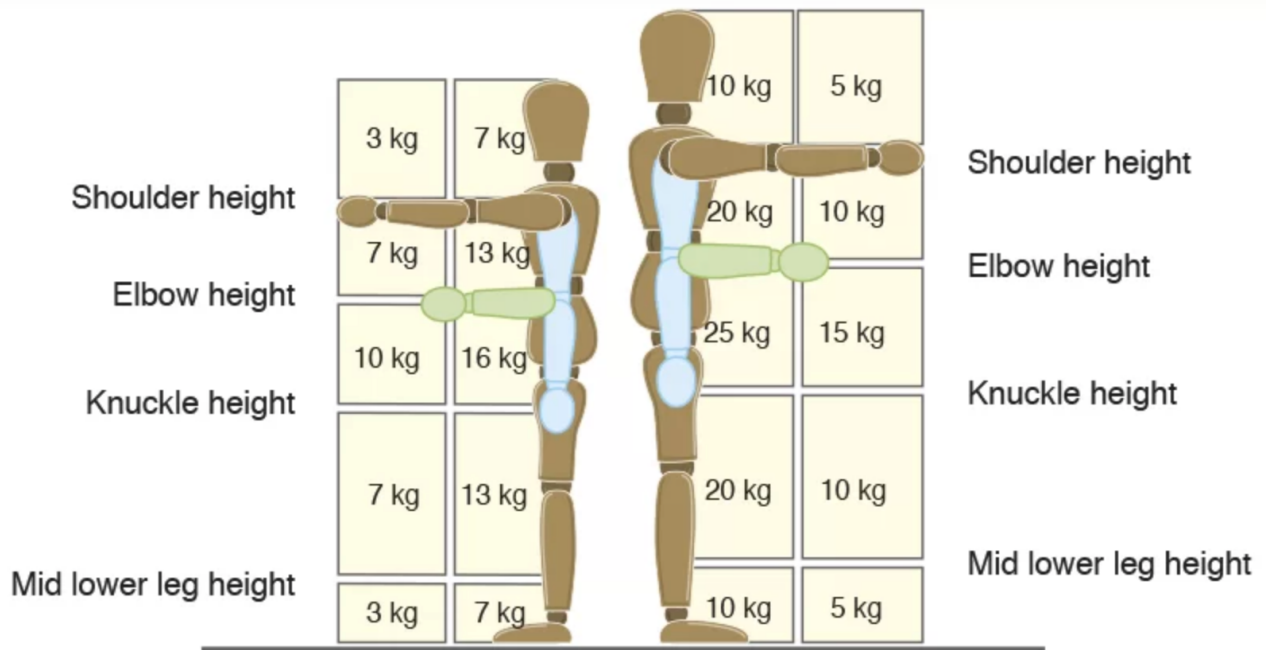

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 19 of 45	M 3

M3 _ M A D E

6.0 WASTE CONTROL

The waste disposal is a major issue. All the M3 operatives must be aware that by minimizing waste by avoiding and reducing waste, and re-using and recycling, we can cut waste by up to 50 percent.

Before starting every working day everyone consider as priority the following points:

Reduce—Avoid waste-look for ways to produce and re-use goods that stop waste being generated.

Re-use—Re-use containers, packaging or waste products.

Recycle—Recycle waste material into useable products.

Dispose of the waste safely.

In general all the M3 operatives have to know that:

- Choose products with recyclable or reusable packaging
- Reuse all types of containers over and over again
- Look for products in reusable, refillable or recyclable packaging when shopping.
- Re-use goods to repaired or replace materials during the installation rather than replaced with new one.
- Use rechargeable batteries rather than single-use batteries and be sure that the old one is disposed properly.
- Use glass bottles and jars, plastic bags, aluminum foil and take away food containers over and over again before recycling or disposing of them.
- Carry lunches in a reusable container rather than disposable wrappings.
- Recycling materials used in construction for further uses. Only recycle after trying to reduce and reuse.

In general all the M3 operatives have to know that on site:

Off cuts and waste – if cannot be reused - will be deposited in bins on the floor provided by the main contractor. M3 will load its waste packaging material and other rubbish to this bins on the floor for subsequent disposal by the main contractor.

M3 is responsible for removing all of their waste from their work area on a daily basis, in an approved and controlled fashion, to the dedicated bins at each floor, which is in keeping with current waste removal regulations and the project logistics strategy. The waste will be removed appropriately and compliantly from site, by others.

Appliances packaging: disposal to the dedicated bins at each floor, which is in keeping with current waste removal regulations and the project logistics strategy.

M3 operatives will be sure to:

- Keeping the workplace clean and tidy at all times
- Minimising the volume of the waste created by work activities

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 20 of 45	M 3

M3 _ M A D E

- Clearing away all rubbish emanating from his workforce
- Removing regularly the waste produced from the workplace to the skips provided by the Company;
- Segregating 'hazardous wastes (i.e. special waste) from 'non-hazardous wastes' for final disposal from site.
- Remove pallets from site in agreement with the site team (at least a load every 10 days)

7.0 COMPETENCY OF THOSE INVOLVED AND EXTERNAL FITTERS

All M3 operatives will provide completed security forms prior to induction if requested by the main contractor.

All operatives will be inducted by the main contractor's site management prior to commencing work.

All site personnel (including Site Manager and Site Supervisor) to hold an appropriate and valid CSCS card. All operatives will have been briefed on this method statement and will have signed the record sheet appended to this method statement.

The Risk Assessment and Method statement must be signed, reviewed and agreed by all the M3 operatives and manager before starting any activity on site. All operatives will have been briefed on this method statement and will have signed the record sheet appended to this method statement.

NO WORKS IS COMMENCED UNTIL ALL THE NECESSARY DOCUMENTS ARE PROVIDED AND ACCEPTED BY THE MAIN CONTRACTOR RELEVANT MANAGER

Any new operatives must be inducted (main contractor) and must have a formal RAMS briefing prior permitted to work on site – this must be recorded on the RAMS

M3 PM/SM IS RESPONSIBLE FOR ENSURING THAT:

All works on site are covered by a RA as a minimum

All medium and high risk works activities on site are covered by a documented MS

The RAMS is produced, reviewed and discussed with all the operatives on site

The RAMS is updated when necessary

The RAMS have to address all of the sequential steps of the activities and all that can be identified as a risk

The significant risk are identified in a safety plan

Any new operatives must be inducted (main contractor) and must have a formal RAMS briefing prior permitted to work on site – this must be recorded on the RAMS

BOTH THE M3 OPERATIVES AND MANAGERS HAVE TO ENSURE THAT:

All the operatives have to wear the correct PPE

The site rules are respected

The welfare facilities are used correctly

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 21 of 45	M 3

M3 – MADE

First Aid arrangement and procedure are in place

If you are using hazardous substances make sure you use and store them correctly;

If we note any substances that may be present in your work area which could affect your health it must be reported to the Main H&S manager

On site, following the induction and the RAMS induction all operatives must be trained on relevant tasks and certified where applicable.

Operatives to be briefed on operations to be undertaken prior to commencement and all operatives will be aware of potential hazards and site conditions in connection with the operation they are carrying out.

All site personnel to hold an appropriate and valid CSCS card. All operatives should wear appropriate PPE as identified within the risk assessment.

CSCS CARD – WORKS THAT YOU CAN DO

The card to allow you to work on site are many and different.

The Carpenter/SM need to be sure to have the correct card for the works you need to do.

JOINER/CARPENTER:

- Approved Indentured Apprenticeship
- Diploma Level 2
- Informal Employer Apprenticeship with a City and Guilds Craft Certificate
- VQ Diploma Level 1
- VQ Diploma Level 2
- VQ Diploma Level 3

LABOURS:

You need to have done the **ONE DAY SITE SAFETY PLUS H&S** awareness certificate

The workers that have a green card as a Labour cannot work on site as a Joiner or carpenter.

This is forbidden by the law,

WORKERS ON SITE MUST DO WORKS IN ACCORDANCE TO THE LEVEL OF THEIR CARDS – NO EXTRA ACTIVITIES ARE ALLOWED IF THEY ARE NOT QUALIFIED FOR THEM.

8.0 PLANT & EQUIPMENT TO BE USED

All plant or equipment will be inspected before use to check for the following:

- Integrity of electrical cables

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 22 of 45	M 3

M3 _ M A D E

- Blades for cutting-off machine (or similar) and table saw (or similar) are fixed properly.
- Safety guard and guide fence for cutting-off machine (or similar) and table saw (or similar) are fixed properly.
- Equipment is generally in good order.

Prior to any plant or equipment being operated on the project for the first time the following must be reviewed by the operatives:

- 1) Thorough Examination Certification – Certification to be reviewed to ensure it is still valid. If certification is out of date the plant / equipment must be quarantined.
- 2) Any plant that requires multiple users must be cleaned after each use.
- 3) Daily and weekly checks must be completed and recorded.

Every worker must be well trained and must be aware of the tools he is using.
The worker is responsible for a bad maintenance or bad use of a cutting machine on site.

Cutting wood will produce dust, and suitable measures will be put in place to minimise exposure, including dust extractors on tools and suitable masks. All operatives will have appropriate face fit testing and respiratory equipment. Dust extraction will be used at all times. Exclusion zones with barriers and appropriate signage will be in place around M3 cutting stations.

Signage will be provided to warn other trades, with vacuums Class M or H standard as per site requirements.

The steps to follow to use a cutting machine/electric tools or similar are:

1. **Read the manual.** Make sure that you are using the right blade and that it's correctly seated and tightened securely. Always wear safety glasses and always use sharp blades because dull blades will bind in the wood and can cause the material to kick back.
2. **Check the blade guard.** Periodic checking for loose bolts is a good idea too. Always use the blade guards. If you need take additional safety precautions.
3. **Make sure the blade and fence are square.** You can test this by drawing a perfectly straight line on a scrap piece of wood parallel to its edge and then cutting the line with the saw.
4. **Avoid wearing jewelry or baggy clothing.** Both of these can be grabbed by the blade if you get too close, damaging them and possibly pulling you towards the blade.
5. **Keep a sensibly low blade height.** A low blade is less dangerous, with less kick back potential. The higher the blade, the fewer teeth are in the wood at any time, causing more friction and more heat and hence far more potential for kick back.
6. **Look for knots and nails or staples in the wood before you begin.** Avoid knots if possible; if they can't be avoided, be cautious when cutting through them.
7. **Start the saw and let it reach maximum RPM before beginning the cut.**
8. **Stand to the side in case the wood is kicked back and be sure the wood is supported on the other side.**
9. **Have a push stick close always to keep your hands away from the blade.** Never over-reach or try to cut a piece that is too long or too wide to be managed easily. Don't

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 23 of 45	M 3

M3 _ M A D E

push the wood into the blade, just feed it into the blade with a little pressure. Forcing the wood causes extra friction and it could kick back.

- 10. Keep the wood firmly against the guide fence as you make the cut.** Use an out-feed table, rollers or an extra person to assist you if you need it.
- 11. Wait for the blade to come to a full stop before removing it from the wood, if you are not cutting all the way through the length of the wood.**
- 12. Wear ear protection.** Table saw motors are extremely noisy, and you risk damaging your ears if you do not protect them. You need always to wear the correct PPE when you are cutting (ear plugs + glasses).

In general all the workers are responsible for the following:

- Use the assigned protective equipment in an effective and safe manner.
- Follow established work procedures as directed by the supervisor.
- Report any unsafe conditions or acts to the supervisor.
- Report any exposure incidents

All electrical equipment will be PAT tested every 3 months and will all be 110V supply.


The first aid kit will be kept in the site office / M3 site box

The nearest Accident and Emergency unit is at the following address:

Queen Elizabeth Hospital,
Stadium Rd, Woolwich,
London SE18 4QH
Tel: 020 8836 6000

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 24 of 45	M 3

M3 _ MADE

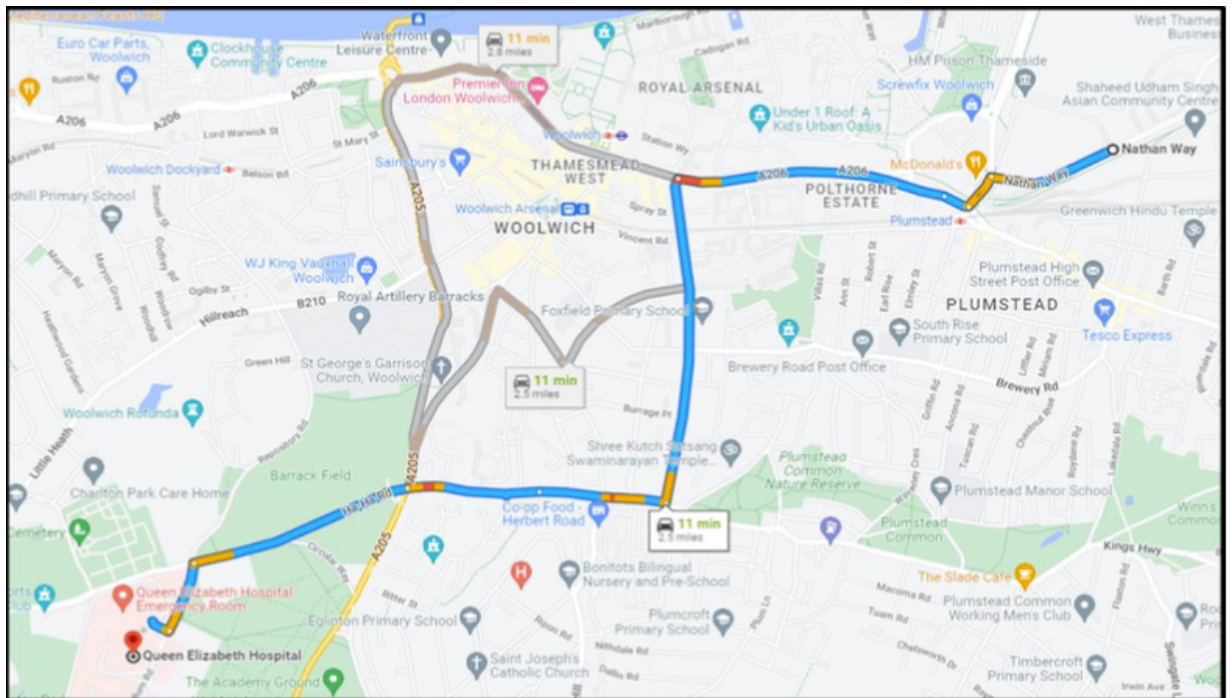

All operatives to be inducted by the main contractor.

Operatives to be briefed on site of fire regulations and evacuation procedures during induction and any changes advised via task briefing or tool box talks.

Fire plan, escape routes and assembly point, to be displayed on the site notice board and at each level by the main contractor.

All accidents should be recorded in the M3 accident book that is kept in the site office / M3 site box. M3 will ensure that an external consultant will visit the site on a regular stage (monthly) to check the H&S matter. A report will be issued to the main Contractor if needed

9.0 COMMUNICATION

Method statements are to be read and understood by all operatives and method statement awareness forms will be signed.

Toolbox talks are to be carried out by M3 on a weekly basis and in the event of any change in circumstances.

M3 representatives will attend main contractor co-ordination meetings as required on site.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 25 of 45	M 3

M3 _ M A D E

10.0 SUPERVISION

The Op Director will be Michele Di Nicola. Any changes will be confirmed before the start of the installation on site.

The Site Manager will be Shaharyar Ali.

The H&S Manager is Peter Wildi – external consultant.

Each work area will have an appointed lead hand who will be responsible for ensuring the work is carried out in accordance with the approved method statement and task sheets.

Daily Activity Briefings will be held with all operatives before starting work. The M3 site manager will give the briefing. This enables the operatives to be assigned tasks and to feedback on any issues regarding safety that may have happened on the previous shift – e.g. changes to work area access.

11.0 MONITORING OF WORK

M3 site management to monitor work being carried out at regular intervals.

M3 have an external consultant in Health & Safety matter that – according to M3 request, arrange visit on site to monitor the work (including statutory inspections, checks and reviews)

12.0 TECHNICAL INFORMATION

All works will be carried out in accordance with good working practice.

Manufacturers recommendations and drawings will be followed.

13.0 3RD PARTY PROTECTION

Attention will be given to the movement of materials and plant and the access onto the site area by operatives with particular attention given to pedestrians passing directly adjacent to the site area.

Non construction third parties should not be present within the site as controlled access will prevent unauthorised access.

14.0 PPE

Generally, refer to control measures and PPE listed within Risk assessments but note that M3 minimum PPE standards include:

- Safety Boots – To be ankle high, with steel toe caps and sole protection.
- Hard Hat with safety tether (Colour coded to relevant role) – Company Logo optional.
- Hi Visibility vest – Branded with M3 logo.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 26 of 45	M 3

M3 _ M A D E

- Safety Gloves – PCN-RED Cut resistant gloves for operatives (Cut Level 1)
- Safety Glasses

Task specific PPE will also be required, including safety glasses and dust masks when cutting at any time and producing dust. FFP3 Disposable masks to be provided by M3 to all carpenters. Must always conform to site rules. All operatives will have appropriate face fit testing and respiratory equipment.

PPE is to be worn at all times and under no circumstances relaxed while on site.

NOTE: Individuals must use their own PPE and not share it with others.

15.0 POWER SUPPLY

110v power will be provided by the main contractor throughout the site via 10kVa transformers.

Leads and splitter boxes will be provided by M3. Leads must be clipped up (out of the way of access route).

It not permitted to use any electrical appliances with exposed elements anywhere on the site. This includes, but is not limited to, toasters, worktop mounted or portable cookers and electric bar or fan heaters.

It is not permitted to use any form of step up transformers on site.

Any components that are damaged or in a poor / unsafe condition will be condemned and must be disconnected & removed from site immediately.

16.0 LIGHTING

Safety lighting will be installed throughout the site by the main contractor as the works proceed. However, when additional task lighting is required, it will be provided by M3. The minimum task lighting requirements where permanent lighting is unavailable must be sufficient to allow the operative to work on site with acceptable visibility. If in doubt, please ask to the Site Manager.

17.0 WORKING PLATFORMS

The following will be used dependent upon purpose and location:

- Lightweight aluminium towers
- Podium Steps
- Hop-ups 600x600mm
- Ladders (separate RA will be provided in case they will be used).

The operatives have to work face on the task when using a stepladder (to be used as a last resort)

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 27 of 45	M 3

M3 _ M A D E

Use appropriate grade of stepladders and hop-ups. **All the equipment must be tagged and inspected every 7 days** and before each use.

Visually check the equipment form damage before use.

Use only on a firm level base

Ensure that equipment is used correctly and in agreement to the manufacturer's instructions.

Inspection of all access equipment is to be done weekly and before each use.

Use only as a very last resort and only once following STG permit system.

18.0 EXCAVATIONS AND TEMPORARY WORKS

- None envisaged

19.0 EMERGENCY PROCEDURES

Emergency procedures will be explained during the site induction.

A summary of changes made to take into consideration the 2m social distancing guidance:

- 1) A one way system has been implemented in places on site, this must be followed unless there is an emergency when people will be required to leave via the nearest exit.
- 2) Fire extinguishers will be placed around the project and welfare facilities. M3 will still be responsible for their own fire extinguishers.

Emergency routes and walkways must be kept clear at all times.

20.0 FIRE

Fire evacuation procedure will be dictated by the main contractor and briefed to M3 operatives at the induction.

M3 will refer to the Fire Safety Plan for the site which will be drawn up prior to commencement and will be contained in the construction phase plan.

In the unlikely event of a fire, M3 operatives will leave the site to the assembly point and await the arrival of the Fire Brigade (all the process will be done according to the procedure instructed during the site induction).

It is considered necessary to set out the following indications:

- *Absolute ban on leaving unattended, for even a short space of time, motorised equipment, or which is under voltage or in any case which may switch on*
- *The obligation to keep the workplace clean by eliminating on a continual basis the formation of waste which may represent a risk of fire*
- *The obligation to have available adequate (in terms of number and features) fire extinguishing devices (extinguishers), which must be kept in good working order in relation to the type of ongoing work. Fire points are located on every floor as indicated on fire plan*

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 28 of 45	M 3

M3 _ M A D E

- *Absolute ban on using naked flames except for normal good practice operating procedures. Hot Works Permits must be obtained from Main Contractor office before hot works are carried out*
- *Absolute ban on leaving gas cylinders or cans (including empty ones), rags doused in inflammable substances and generally inflammable material except at the prearranged deposit points*
- *Absolute ban on leaving electric cables (even if not live) unattended on the ground or on structures*
- *Absolute ban on leaving lamps lit (even if protected and legally compliant) in rest periods, even if short*
- *Obligation to constantly air rooms in any work situation*
- *Do not deposit materials along security passage ways or exits especially fire exit routes*

FIRE CLASS:

CLASS A: Includes all solid, combustible or inflammable materials, which leave embers and which are difficult to extinguish (wood, materials, paper, rubber, etc.).

The extinguishing substance, generally water, must be able to be used on the incandescent mass and not just on the flame.

CLASS B: Includes all inflammable liquids (paints, alcohol, lacquers, petrol, etc.). Generally foam, powder and halogenated gases are used as the extinguishing substance.

CLASS C: Includes all gaseous materials (butane, propane, methane, hydrogen, etc.).
Water, powder and halogenated gases are used as the extinguishing agent.

CLASS D: Includes all light combustible metals (aluminium, magnesium, sodium, potassium, etc.) and are very hard to extinguish owing to their ability to oxidise.
Special powders must be used to extinguish fires of this type.

CLASS E: Electrical equipment fires.
(transformers, switches, electrical panels and electrical equipment generally)

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 29 of 45	M 3

M3 _ M A D E

Symbols:



General rules on the use of extinguishers

Some indications are given on the correct use of portable fire extinguishers.

	Flames and smoke make the fire difficult to put out, therefore it is necessary to position yourself with the wind on your back in relation to the fire and put it out from top to bottom
	Do not use the extinguisher randomly, but always from top to bottom
	For a small size fire turn off the extinguisher only when the fire is out and use the remainder to make the area safe
	An average size fire must never be tackled if one is alone, but several extinguishers must be used, attacking the flames at the same time from several directions by bringing the jets together but without being opposite one another
	In the case of liquid contents in drums, the surface of the liquid must not be hit, as the liquid may pour out, but try to interrupt the flames to suffocate the fire

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 30 of 45	M 3

M3 _ M A D E

	<i>Once the extinguisher has been used, whether empty or half full, it must never be put back in its place, but it must be refilled</i>
---	---

21.0 1st AID

Since it is essential not to waste time in emergencies, it is fundamental to adopt some simple measures to facilitate adequate and timely action.

It should be recalled that **no one is obliged by law to put their own safety at risk** to offer assistance and must not worsen the situation with inappropriate actions or behaviour.

In particular, during the stages of first aid:

- *Do not subject the injured person to unnecessary movement*
- *Absolutely do not move people with head or spine trauma and those with suspected broken bones*
- *Do not press or massage the person when the event may cause deep injuries*
- *Do not administer drinks or other substances*
- *Loosen clothing which may hinder breathing*
- *If the injured person is not breathing, artificial respiration may be tried by someone capable of doing so*
- *Use call points located on site to call for First Aid assistance if required*

22.0 SPECIAL CONTROL MEASURES

It is not envisaged that M3 activities on the site will require special control measures (i.e. permit to work systems, specialist training, specialist equipment etc) to ensure the adequate protection of employees and/or others against risk of injury. If required, it will be requested a special permit for the ladders.

23.0 APPROVAL, REVIEW and BRIEFING

This method statement must be approved by the main contractor's project manager before work can commence. A record of the signed off approval sheet will be kept in the site office / M3 site box.

If a change in work method is required then the method statement must be reviewed, altered and re briefed as required.

All operatives will be briefed on this method statement and will sign the record of briefing sheet (**Appendix 3**).

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 31 of 45	M 3

M3 _ M A D E

24.0 APPENDICES

The following documents are appended to this method statement

Appendix 1 - Risk Assessments

Appendix 2 – Manual handling assessment – Operate a pallet Truck – Cutting on Site and Lone Worker assessment

Appendix 3 – Method Statement Briefing Register

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 32 of 45	M 3

M3 _ M A D E

Risk Assessment

	RA No:	RISK ASSESSMENT	APPENDIX 1
	Project: London Dock Block G	Work Area: Pennington Street, Wapping, London, E1W 2BD	
	Task: Kitchen package	Job No:	
	Date: 05/08/2026	Review Date:	05/11/2026
	Completed by: M. Di Nicola	Signature: 	

Risk Assessment

Project Name & No	London Dock Block G	Risk Assessment Number	Rev 00	Date	5/8/2026
Location	Pennington Street, Wapping, London, E1W 2BD				
Activity	Kitchen Installation				
Persons Exposed	Fitter and Labours				

Likelihood	Frequent	Probable	Occasional	Improbable	Incredible
	5	4	3	2	1

Severity	Catastrophic	Major	Serious	Significant	Minor
	5	4	3	2	1

RISK RATING = LIKELIHOOD X SEVERITY

Potential for Harm	Low (L)	Medium (M)	High (H)
RR Value	1 to 4	5 to 15	16 to 25
	No additional controls required	Efforts should be made to reduce the risk	Work should not be started until the risk has been reduced

Hazard	Likelihood	Severity	Initial Risk Rating (RR)	Controls	Likelihood	Severity	Residual Risk Rating (RR)
Skin Irritation/Infections (from the use of substances)	2	4	8	COSHH assessment to be carried out and controls implemented (if required). Use of the correct PPE	1	4	4
Dust	4	4	16	Good Hygiene. When using handsaws, the area must have general ventilation, when using power saws extractor/hover must be in place. Adequate dust mask to be worn when cutting and sanding (please refer to MS for the type of PPE to be used). Adequate ventilation and extract/vacuum (class M as a minimum) fitted to tools and saws.	1	4	4
Noise in workplace	2	4	8	Noise assessments will be undertaken if necessary. Adequate PPE to be used	1	4	4
Blades/sharp edges from cutting tools (skill saw, jigsaw, Router, festool, hand saw etc)	4	4	16	Separate cutting areas where necessary with adequate signage. Use the right tool for the job and use the tool only for the job it is designed for. Educate and train the staff in the safe use of any tool. Inspect the tools before use and follow the manufacture instructions. Use the safeguard. Cut on a stable surface	1	4	4
Slips and trips	3	4	12	Good housekeeping to be maintained. Wear suitable personal protective equipment as detailed below.	1	4	4
Dermatitis or other skin infections	3	4	12	Gloves (EN 420) to be worn to protect against skin infection, cuts, abrasions and splinters. Substitution of the hazardous substances with less one.	1	4	4
Manual handling (see also the RA below)	4	4	16	Good manual handling techniques should be adopted. Regular Manual Handling toolbox talks will be provided (to carry out a Manual Handling toolbox talk to any new starter, e.g after induction and RAMS briefing). Reduce manual handling	1	4	4
Falls from height	3	4	12	Suitable access equipment to be selected when working at height for example podiums steps or mobile towers. Edge protection and handrail to be used. Robust and secure working platforms and/or podium stairs to meet requirements under GMR 4.1 and the relevant EDRs 'Working at Height'. This is to also be considered and incorporated when looking at vehicle delivery and offloading methodology if necessary	1	4	4
Contact/crushing of hand/fingers from hand tools such as hammers and Electrical	3	4	12	Operatives that use these tools must be trained. All tools must be PAT tested and regularly tested. Operatives to carry out a visual inspection of the tool prior to use. Any defective tools must be reported to the managers and remove from use. PPE used need to be suitable for work activity being undertaken. Where possible components are to be manufactured to size off site; in instances where on site cutting is required separate dedicated cutting workshop to be established.	1	4	4
Use of small hand tools	3	3	9	All operatives that are to be used for the stair protection works are experience labour and competent to undertake the protection tasks. Operatives carry out a visual inspection of the tool prior to use. Any defective tools must be reported to the managers and remove from use. Check tool is appropriate for the job and used in accordance with manufacturer's instructions. All PPE must be used	1	3	3
Manual Handling of materials that cannot go in the hoist, storage of materials & distribution of goods	3	4	12	Material to be delivered in a 'just in time' manner to limit the requirement to store on site. Material to be stored in agreed locations in a safe manner. In the event of an evacuation the materials being carried are to be taken back down and out of the building and left away from the escape entrance. Operatives will use mechanical methods of lifting and handling materials as far as practical	1	4	4
Delivery & unloading of materials with risk of reversing vehicles and dropping load	3	4	12	No temporary storage of materials directly in front of the escape doors. FORS Silver Vehicle to have reversing alarm and be directed to designated unloading zone. The vehicles will be directed in the delivery area following the banksman indication (Banksman provided by main contractor). No access to the rear of the vehicle without protection if needed	1	4	4
Vehicle and Plant Incident	3	4	12	Risk of interface with construction vehicles when offloading vehicles and transporting materials. All vehicles to have edge protection if requiring personnel to access the vehicle to offload. All vehicles to have materials pre-slung if requiring crane lift and to have a full robust No Person zone around the vehicle during the offloading	1	4	4
Abrasive Wheels	3	4	12	No person may be permitted to mount abrasive wheels unless he has been trained and holds a Certificate of Appointment. Only nominated/competent/trained persons must be change wheel/disc. Only trained certificated personnel are permitted to use abrasive wheels. The tools must be inspected prior to use them. PPE to be used correctly	1	4	4

Risk Assessment							
Project Name & No	London Dock Block G			Risk Assessment Number	Rev 00	Date	5/8/2026
Disposal of Waste, Recycling	3	4	12	Disposal of COSHH material as suppliers Safety data sheets; Ensure that the allocated waste bins are being used for COSHH waste; Timber Crates will be broken down flat de-nailed and removed to designated recycling skip at CC; All Waste materials will be removed to the designated recycling bins	1		
Use of substances hazardous to health	3	4	12	Consideration should be given to: •Use of alternative substances that are less harmful •Ensuring work areas are well ventilated to allow fumes to disperse •Follow the COSHH assessment	1		
Emergency Procedures (Unable to obtain first aid, failure to evacuate building)	3	4		All operative to undergo site Induction to ensure operative know location of nearest first aid and how to identify project first aid. Identify at site induction Safe routes, Emergency Exit, Fire Marshall and Muster Point; Notified any updates changes to above on site notice boards; Out of hours working permit to be in place; No alone working.	1		
Possible contact with 230V during installation and temporary electrics	4	5	20	All the installer must be instructed to not work in the vicinity of live services unprotected. All the areas must have a signage that identify the risk. M-CONTRACT is not connecting anything to the main power. M-CONTRACT operative only connect the LED to the driver. No work that involve any contact with live cables must to be carried out. Permit systems and procedures required to control access and working methods when in proximity to live electrical systems. All operatives to be suitably trained and qualified. All electrical powered plant and tools to be PAT tested and valid	1		
Failures of Fixtures & Fittings	3	4	12	A full fixing review must be done. This will outline all types of fixture and components involved and in which condition these are to be used. This will avoid incorrect fittings being used in differing conditions.	1		
Proximity of adjacent residents and occupiers	3	4	12	Hours of working to be strictly adhered to. Community liaison set up by Main Contractor to field any concerns of the public.	1		
Extreme temperatures or climatic conditions	3	4	12	Special precautions to be agreed with Main Contractor and implemented as required.	1		
Drops Prevention Plan (Material & tools)	3	4	12	Loose fixtures and fixings to be captivated as far as reasonably practicable in the design and planning stage to reduce the volume of loose fixings at the worksite. Primary controls to be in place when working at height to control fall of tools & equipment – ALL TOOLS REQUIRED TO BE FULLY TETHERED WHEN WORKING AT HEIGHT	1		
Hazards due to movement of plant and materials	3	4	12	Close coordination needed with services Trade Contractors. Logistics, access arrangements, protection of installations and exclusion zones to be agreed at an early stage.	1		
Lifting Activities	3	4	12	Lifting activities to be planned via Lifting Plans by an Appointed Person. Lifting supervisors to oversee the lifting activities at all times. Operator certification of competence and training. M-CONTRACT will be involved in supervision of the unloading of joinery components (wardrobes, doors, floor finishes) – N/A on this site	1		
			12				
			12				
			12				
			12				
			12				
			12				
			12				
Other Relevant Information							
COSHH Assessment	Notes Assessment	PPE Assessment	Manual Handling Assessment	Training Requirements	HAVs Assessment	Other Information	
			Please Ref to RAMS (Manual handling Assessment)				
Please refer to COSHH Assessment in the RAMS							

Prepared by			
Name	Michele Di Nicola	Title	Operation Director
Date	5/8/2026	Signature	Michele Di Nicola

Approved by			
Name		Title	
Date		Signature	

Risk Assessment	
-----------------	--

Date: 05/08/2026
Review Date: 05/11/2026

Review Date: 05/11/2026

JOB/TASK:	Sustainability and Environmental Hazards
------------------	--

Sheet: 1 of 1

Assessor: M. Di Nicola

RA No: _____
ASite Document No: _____

ASite Document No:

Persons Effected :	Employees		X	Contractors	X	Client Employees			Public	
--------------------	-----------	--	---	-------------	---	------------------	--	--	--------	--

STANDARD CONTROL MEASURES	
1	1.1
2	2.1
3	3.1
4	4.1
5	5.1
6	6.1
7	7.1
8	8.1
9	9.1
10	10.1
11	11.1
12	12.1
13	13.1
14	14.1
15	15.1
16	16.1
17	17.1
18	18.1
19	19.1
20	20.1
21	21.1
22	22.1
23	23.1
24	24.1
25	25.1
26	26.1
27	27.1
28	28.1
29	29.1
30	30.1
31	31.1
32	32.1
33	33.1
34	34.1
35	35.1
36	36.1
37	37.1
38	38.1
39	39.1
40	40.1
41	41.1
42	42.1
43	43.1
44	44.1
45	45.1
46	46.1
47	47.1
48	48.1
49	49.1
50	50.1
51	51.1
52	52.1
53	53.1
54	54.1
55	55.1
56	56.1
57	57.1
58	58.1
59	59.1
60	60.1
61	61.1
62	62.1
63	63.1
64	64.1
65	65.1
66	66.1
67	67.1
68	68.1
69	69.1
70	70.1
71	71.1
72	72.1
73	73.1
74	74.1
75	75.1
76	76.1
77	77.1
78	78.1
79	79.1
80	80.1
81	81.1
82	82.1
83	83.1
84	84.1
85	85.1
86	86.1
87	87.1
88	88.1
89	89.1
90	90.1
91	91.1
92	92.1
93	93.1
94	94.1
95	95.1
96	96.1
97	97.1
98	98.1
99	99.1
100	100.1

Risk Assessment Matrix

SEVERITY		LIKELIHOOD
No Injury	1	Almost Never
Minor Injury	2	Seldom
7 Day Injury	3	Possible
Major Injury	4	Probable
Death	5	Frequently

[illegible]

M3 _ M A D E

MANUAL HANDLING ASSESSMENT			APPENDIX 2		
Task title and location:			MANUAL HANDLING TO MOVE GOODS ON SITE		
Assessed by:			MDN	Date assessed:	05/08/2026
Assessment factor	Degree of risk			Hazards	Control Measure
	Low	Med	High		
Task Assessment: - Holding or manipulating loads away from the STGry and excessive lifting, lowering, carrying distances or strenuous pushing or pulling? - Risk of unpredictable movement of loads? - Repetitive handling or frequent or prolonged physical effort?		M		Back injuries/hernias/ruptures	Adjust the posture and unload the good with minimum 2 labours
		M	H	Problem to move the goods safely/accidents Injuries/damages on goods	To split the load or use the correct equipment (pallet truck) To involve two or more people or use a correct equipment (Pallets truck, trolleys. Please check the table of weight limit)

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 34 of 45	M3

M3 _ M A D E

Loads - are they: • Heavy, bulky or unwieldy? • Difficult to grasp, unstable or unpredictable with contents likely to shift?		M	H	To damage the goods or to risk of injury Material can fall down	To split the load in smaller loads or use more people To use an adequate handhold. Always use the correct PPE for the task (Gloves)
Work environment - are there: • Space constraints preventing good posture, uneven, slippery or unstable floor? Variations in the levels of floors or work surfaces?		M		Material to be moved up and down the ramps (1:10 ratio GF to hoist)	To split the loads (for example the goods loaded on the pallets) in smaller loads and use more people and the correct equipment
Individual Capacity - does the job: • Require unusual strength, height or capability?		M		Back Injuries	Split the loads if possible/ team lifting to be same size and built as yourself to maintain the balance

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 35 of 45	M3

M3 _ M A D E

MANUAL HANDLING ASSESSMENT		APPENDIX 2				
Task title and location:		OPERATE A PALLET TRUCK				
Assessed by:		MDN		Date assessed: 05/08/2026		
Assessment factor	Degree of risk			Hazards	Control Measure	
	Low	Med	High			
Task Assessment: - Enter the pallet truck to load the goods - Move the pallet truck once loaded - Heavy load or frequent or prolonged physical effort? - Route not clear from obstacles - Route not straight			M		Back load not securely stacked.	Check the load is securely stacked and the pallet truck is not damaged
				H	Problem to move the goods safely/accidents	Ensure sufficient space between operator and there is enough clearance when raising the forks
			M		Injuries/damages on goods	To involve two or more people or use a correct equipment
			M		Problem to move the goods safely/accidents	Face the direction you will be travelling, ensure the route is clear from obstruction.
			M		Problem to move the goods safely/accidents	Never run. When travelling down a slope with the pallet truck loaded, keep the load facing down and control the speed by pulling back with both hands on the handles

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 36 of 45	M3

M3 _ M A D E

Off loading of the goods		M		Injuries/damages on goods	ensure you are clear of the load before lowering by slowly pulling on the lever, Pallet truck must have breaks When fully lowered release the lever into the neutral position Check all around is clear and pull the hand pallet truck clear of the pallet.
--	--	---	--	---------------------------	--

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 37 of 45	M3

M3 _ MADE

DUST ASSESSMENT	APPENDIX 2				
Task title and location:	CUTTING ON SITE				
Assessed by:	MDN			Date assessed:	05/08/2026
Assessment factor	Degree of risk			Hazards	Control Measure
	Low	Med	High		
Task Assessment: • Dust following the cutting on site 					

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 38 of 45	M3

M3 _ M A D E

• Blades/sharp edges from cutting tools (skill saw, jigsaw, Router, festool, hand saw etc) • Noise produced following the cutting on site • Maintenance and use of the right equipment		M		Cut, infection, blood loss, amputation	Separate cutting areas where necessary with adequate signage. Use the right tool for the job and use the tool only for the job it is designed for, Educate and train the staff in the safe use of any tool, inspect the tools before use and follow the manufacture instructions, Use the safeguard, Cut on a stable surface. Always use the blade guard.
		M		Permanent hearing loss, tinnitus or other hearing-related conditions	Table saw motors or similar tools are extremely noisy, and you risk damaging your ears if you do not protect them. You need always to wear the correct PPE when you are cutting (ear plugs + glasses).
		M		Damages to the product and injuries	Make sure that you are using the right blade and that it's correctly seated and tightened securely. Always wear safety glasses and always use sharp blades because dull blades will bind in the wood and can cause the material to kick back.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 39 of 45	M3

M3 _ M A D E

Cutting wood with power tools		M		Injury/death	Avoid wearing jewelry or baggy clothing. Both of these can be grabbed by the blade if you get too close, damaging them and possibly pulling you towards the blade. Look for knots and nails or staples in the wood before you begin. Avoid knots if possible; if they can't be avoided, be cautious when cutting through them. Never over-reach or try to cut a piece that is too long or too wide to be managed easily. Don't push the wood into the blade, just feed it into the blade with a little pressure. Forcing the wood causes extra friction and it could kick back.
---	--	---	--	--------------	--

M3 _ MADE

LONE WORKER ASSESSMENT		APPENDIX 2			
Task title and location:		LONE WORKER			
Assessed by:		MDN		Date assessed: 05/08/2026	
Assessment factor	Degree of risk			Hazards	Control Measure
	Low	Med	High		
Task Assessment: Is the employee subject to any medical condition that may place them at increased risk when working alone?			M	Back injuries/death	The employee must ensure that any medical conditions which might be relevant to their working alone are fully discussed with their line manager and, if necessary, Occupational Health and own GP. Individuals must not work alone if any such condition is assessed as placing them at increased risk. Any person who requires assistance to get out of the building in an emergency must not work alone.
Lone working on site – access and emergency procedures			M	Fire, personal injury, other emergency situations	The employee must comply with the out-of-hours log-in/out arrangements in operation within the site. Set up contact arrangements with staff and family members. Lone workers must be

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 41 of 45	M3

M3 _ M A D E

Travel to and from site and working in a building out of hours		M		Personal safety and security	experienced and have permission from their Supervisor / line manager in order to lone work. He must be aware of the emergency control measures, e.g. fire evacuation procedures, how to call for a first aider, location of first aid box etc. People are advised to take basic precautions, such as informing the supervisor when they are leaving the site, arranging to walk to the car park with a colleague and not taking short cuts
Slip/trips/falls			H	To damage the goods or to risk of injury	Regular inspection of site to ensure that any trip hazards [torn carpets, uneven flooring, trailing cables, etc.] receive prompt attention. Individuals with temporarily impaired mobility must not work alone.

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 42 of 45	M3

M3 _ M A D E

• Electrical equipment		M		Risk of electrocution/Death	Ensure all equipment is electrically tested in accordance with recognised procedures. Electrical cables and plugs visually inspected for damage. Do not interfere with plugs or power supply.
• Work with hazardous substances		M		Health issues/death/injury	Not permitted/specific risk assessment and procedures to be in place
• Single-handed lifting or handling of any load that is of such a weight as to cause injury			H	Back injury	Not permitted/specific risk assessment and procedures to be in place

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 43 of 45	M3

M3 _ MADE

Method Statement Risk assessment and COSSH Briefing Register

[illegible]

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 44 of 45	M3

M3 _ MADE

[illegible]

Issue Date: Aug 2026	LD Block G	Rev 00
Author: M. Di Nicola	Page 45 of 45	M3

M3 _ M A D E

Date of Assessment:		05/08/2026	
SUBSTANCE			
Name of Substance:		MDF Boards or Wood (dust created from cutting MDF boards or wood)	
Supplier:		Various	
Hazardous ingredients in the substance		Wood dust generated when cutting boards/woods	
Chemical Labelling (Check for symbol on the product data sheet or packaging)			
 	 	 	
☒ Toxic/Very Toxic	☒ Harmful/Irritant	☐ Corrosive	☒ Long term health hazards such as cancer
 	 	 	 
☐ Explosive	☐ Oxidizing	☐ Flammable	☐ Tóxic to the environment
Does the substance react with any other substances?		No	
WEL (Work Limit Exposure) of the product			
Risk Phrases Safety Phrases		WEL	
R23/24/25 Toxic by Inhalation, contact with skin and if swallowed R40 limited evidence of a carcinogenic effect R43 May cause sensitization skin contact		Formaldehyde 2.5mg.m3 long term exposure (8hr TWA) 2.5mg.m3 short term exposure (15min) Isocyanates 0.02g.m3 long term exposure (8hr TWA) 0.07mg.m3 short term exposure (15min)	
Substance hazard for health			
Body contact	Effect		
☒ Contact with skin	Toxic		
☒ Contact with eyes	Harmful		

M3 _ M A D E

☒ Breathed in	Toxic			
☒ Swallowed	Toxic			
☐ Injected				
FREQUENCY AND DURATION				
Amount used: Small (ml) How many time per day: 1-5 Duration: 1-5 Minutes				
WHO MIGHT BE HARMED				
Who is exposed to the substance		The operative		
Additional risks to certain groups or individuals		No		
What is the substance used for		Wardrobe installation and Kitchen installation		
Frequency of exposure		Daily		
CONTROL MEASURES				
EXISTING CONTROLS				
Design and use of appropriate work methods		If possible always cut in ventilated areas. Always use mounted extractor.. When cleaning the working area do not sweep the dust, use the hoover or dust extractor. Use the correct PPE		
ADDITIONAL CONTROLS				
Controls required for this substance		Always use the dust mask for cutting, cleaning dusty areas, or clean dust extractor equipment. Work in well-ventilated area. Do not breathe the dust. Avoid contact with skin. Do not smoke, eat or drink whilst handling this product.		
PPE required when using the substance				
				
Eye Protection	Safety Gloves	Respiratory Protection	Overalls/clothing	Other
✓	✓	✓	✓	✓
Safety goggles		Mask with P3 filter	Protect against skin contact	Closed footwear
People using this substance have been provided with information or training on its use		☒ Yes ☐ No		
FIRST AID ACTION				
If contact with skin	Wash immediately with soap and water. Remove contaminated clothing.			
If contact with eyes	Bathe the eye in running water for 10 minutes. Obtain medical attention			
If inhaled	Remove victim to well-ventilated area. Keep warm			

M3 _ M A D E

If swallowed				
Other				
OTHER PRECAUTIONS				
Storage	No special measures necessary			
Spillage	No special measures necessary			
Disposal	Dispose as general construction waste			
In case of a fire	Follow the fire procedure			
Health Surveillance	Keep exposure below WEL; health and working history questionnaire and lung function tests			
RISK RATING FOLLOWING ADDITIONAL CONTROLS				
Hazards remaining	Effect	Likelihood	Severity	Risk
Skin contact	Dryness and cracking	1	2	2
Contact with eyes	Irritation	1	1	1
Inhalation	<i>Long Effetc</i>	1	4	4
Prolonged or repeated contact				
Risk rated: 1-4 = low, 5-8 = medium, 9-15 = high				
All hazards are adequately controlled with all control measures in place		☒ Yes – Proceed ☐ No – DO NOT PROCEED with the use of this substance		
Assessors Name Michele Di Nicola		Date 05/08/2026		

M3 _ M A D E

Date of Assessment:		05/08/2026	
SUBSTANCE			
Name of Substance:		<i>Evo-Stik Grip fill Adhesive Mixture or similar</i>	
Supplier:		EVO-STIK GRIPFILL	
Hazardous ingredients in the substance		Adhesive: Acetone - NAPHTHA (PETROLEUM), HYDRODESULFURIZED LIGHT, DEAROMATIZED; NAPHTHA (PETROLEUM), HYDROTREATED LIGHT, N-HEXANE, XYLENE	
Chemical Labelling			
(Check for symbol on the product data sheet or packaging)			
 	 	 	
☐ Toxic/ <i>Very Toxic</i>	☒ Harmful/Irritant	☐ Corrosive	☐ Long term health hazards such as cancer
 	 	 	 
☐ Explosive	☐ Oxidizing	☒ Flammable	☐ Tóxic to the environment
Does the substance react with any other substances?		No data available	
WEL (Work Limit Exposure) of the product			
Risk Phrases Safety Phrases		WEL	
Name	STD	TWA - 8 Hrs	STEL - 15 Min
ACETONE	WEL	500 ppm 1210 mg/m3	1500 ppm 3620 mg/m3
N-HEXANE	WEL	20 ppm 72 mg/m3	
XYLENE	WEL	50 ppm(Sk) 220 mg/m3(Sk)	100 ppm(Sk) 441 mg/m3(Sk)
WEL = Workplace Exposure Limit. Ingredient Comments WEL = Workplace Exposure Limits			

M3 _ M A D E


Substance hazard for health	
Body contact	Effect
☒ Inhalation	No specific symptoms noted - Vapour may irritate respiratory system or lungs. Vapour may affect central nervous system and cause headache, discomfort, vomiting or intoxication.
☒ Ingestion	No specific symptoms noted - May cause discomfort if swallowed. Pneumonia may be the result if vomited material containing solvents reaches the lungs
☒ Skin contact	No specific symptoms noted - Irritating to skin
☒ Eye contact	No specific symptoms noted - May cause temporary eye irritation
☐ Injected	
Health Warnings: Pneumonia may be the result if vomited material containing solvents reaches the lungs.	
FREQUENCY AND DURATION	
N/A	
WHO MIGHT BE HARMED	
Who is exposed to the substance	The operative
Additional risks to certain groups or individuals	No
What is the substance used for	Wardrobe installation and Kitchen installation
Frequency of exposure	Daily
CONTROL MEASURES	
EXISTING CONTROLS	
Design and use of appropriate work methods	Personal precaution, PPE and Emergency procedures: Avoid skin and eye contact. Ensure adequate ventilation. Wear personal protective equipment. Wear self contained breathing apparatus. Avoid breathing vapour
ADDITIONAL CONTROLS	
Controls required for this substance	Environmental control: Prevent entry into drains and water courses. Methods and material for containment and cleaning up: Wear necessary protective equipment. Extinguish all ignition sources. Avoid sparks, flames, heat and smoking. Ventilate. Absorb onto sand, earth or absorbent granules. Pick up with non-sparking tools and place into metal containers with sealable lids. Mark containers with details of hazards and store in designated area ready for disposal. Runoff or release to sewer, waterway or ground is forbidden
PPE required when using the substance	

M3 _ M A D E

				
Eye Protection	Safety Gloves	Respiratory Protection	Ventilation	Other
✓	✓	✓	✓	✓
Safety goggles	Safety Gloves	Mask with P3 filter	Ventilation	Closed footwear
People using this substance have been provided with information or training on its use		☒ Yes ☐ No		
FIRST AID ACTION				
If contact with skin	Promptly flush contaminated skin with water. Promptly remove clothing if soaked through and flush the skin with water. Get medical attention if irritation persists after washing.			
If contact with eyes	Rinse the eye with water immediately. Continue to rinse for at least 15 minutes and get medical attention			
If inhaled	Move the exposed person to fresh air at once. Get medical attention if any discomfort continues.			
If swallowed	DO NOT induce vomiting. Get medical attention immediately			
Other				
OTHER PRECAUTIONS				
Storage	Keep away from heat, sparks and open flame. Provide good ventilation. Avoid spilling, skin and eye contact. Avoid acids, moisture, and combustible materials. Flammable/combustible - Keep away from oxidisers, heat and flames. Isolate from other materials. Store in tightly closed original container in a dry, cool and well-ventilated place. Ground container and transfer equipment to eliminate static electric sparks. Storage Class Flammable liquid storage			
Spillage	Prevent entry into drains and water courses.			
Disposal	This material is classified as special waste as defined by Special Waste Regulations 1996 and must be disposed of by an authorised contractor			
In case of a fire	Follow the fire procedure			
Health Surveillance	Keep exposure below WEL			
RISK RATING FOLLOWING ADDITIONAL CONTROLS				
Hazards remaining	Effect	Likelihood	Severity	Risk
Skin contact	Dryness and cracking	1	2	2
Contact with eyes	Irritation	2	2	3
Inhalation	Long Effect	1	4	4

M3 _ MADE

Swallowed	Irritation	1	4	4
Risk rated: 1-4 = low, 5-8 = medium, 9-15 = high				
All hazards are adequately controlled with all control measures in place		☒ Yes – Proceed ☐ No – DO NOT PROCEED with the use of this substance		
Assessors Name Michele Di Nicola		Date 05/08/2026		

Date of Assessment:		05/08/2026	
SUBSTANCE			
Name of Substance:		MITREBOND ACTIVATOR (or similar)	
Supplier:		Unika Color Products Ltd	
Hazardous ingredients in the substance		PROPANE- HEPTANE- BUTANE- ISOBUTANE	
Chemical Labelling (Check for symbol on the product data sheet or packaging)			
   	   		
☐ Toxic/Very Toxic	☒ Harmful/Irritant	☐ Corrosive	☐ Long term health hazards such as cancer
   	   		
☐ Explosive	☐ Oxidizing	☒ Flammable	☒ Tóxic to the environment
Does the substance react with any other substances?		In use, may form flammable / explosive dust-air mixture. Extremely flammable. In combustion emits toxic fumes. Forms explosive air-vapour mixture. Vapour may travel considerable distance to source of ignition and flash back. Reactivity: Stable under recommended transport or storage conditions. In combustion emits toxic fumes.	
WEL (Work Limit Exposure) of the product			
Risk Phrases Safety Phrases		WEL	

M3 _ M A D E

PROPANE

Workplace exposure limits:

Respirable dust

State	8 hour TWA	15 min. STEL	8 hour TWA	15 min. STEL
UK	1800 mg/m3	7200 mg/m3	-	-

HEPTANE

UK	2100 mg/m3	8400 mg/m3	-	-
----	------------	------------	---	---

BUTANE

UK	1450 mg/m3	1810 mg/m3	-	-
----	------------	------------	---	---

ISOBUTANE

UK	2400 mg/m3	9600 mg/m3	-	-
----	------------	------------	---	---

Substance hazard for health

Body contact	Effect
☒ Inhalation	There may be irritation of the throat with a feeling of tightness in the chest. Exposure may cause coughing or wheezing.
☒ Ingestion	There may be soreness and redness of the mouth and throat.
☒ Skin contact	There may be irritation and redness at the site of contact.
☒ Eye contact	There may be irritation and redness. The eyes may water profusely.
☐ Injected	

FREQUENCY AND DURATION

N/A

WHO MIGHT BE HARMED

Who is exposed to the substance	The operative
Additional risks to certain groups or individuals	No
What is the substance used for	Wardrobe installation and Kitchen installation
Frequency of exposure	Daily

CONTROL MEASURES

EXISTING CONTROLS

Design and use of appropriate work methods	Respiratory protection: Self-contained breathing apparatus must be available in case of emergency. Hand protection: Protective gloves. Eye protection: Safety glasses. Ensure eye bath is to hand. Skin protection: Protective clothing.
--	---

ADDITIONAL CONTROLS

M3 _ M A D E

Controls required for this substance		Engineering measures: Ensure there is sufficient ventilation of the area. Ensure lighting and electrical equipment are not a source of ignition. Conditions to avoid: Heat. Materials to avoid: Strong oxidising agents. Strong acids.		
PPE required when using the substance				
				
Eye Protection	Safety Gloves	Respiratory Protection	Ventilation	Other
✓	✓	✓	✓	✓
Safety goggles	Safety Gloves	Self-contained breathing apparatus must be available in case of emergency	Ensure there is sufficient ventilation of the area	Closed footwear
People using this substance have been provided with information or training on its use		☒ Yes ☐ No		
FIRST AID ACTION				
If contact with skin	Remove all contaminated clothes and footwear immediately unless stuck to skin. Drench the affected skin with running water for 10 minutes or longer if substance is still on skin.			
If contact with eyes	Bathe the eye with running water for 15 minutes. Consult a doctor.			
If inhaled	Move to fresh air in case of accidental inhalation of vapours.			
If swallowed	Do not induce vomiting. Consult a doctor.			
Other				
OTHER PRECAUTIONS				
Storage	Store in a cool, well ventilated area. Keep container tightly closed. The floor of the storage room must be impermeable to prevent the escape of liquids. Must only be kept in original packaging.			
Spillage	Do not discharge into drains or rivers. Contain the spillage using bunding. Absorb into dry earth or sand. Transfer to a closable, labelled salvage container for disposal by an appropriate method.			
Disposal	Transfer to a suitable container and arrange for collection by specialised disposal company. The user's attention is drawn to the possible existence of regional or national regulations regarding disposal.			
In case of a fire	Advice for fire-fighters: Wear self-contained breathing apparatus. Wear protective clothing to prevent contact with skin and eyes.			
Health Surveillance	Immediate effects can be expected after short-term exposure. Eye bathing equipment should be available on the premises.			
RISK RATING FOLLOWING ADDITIONAL CONTROLS				
Hazards remaining	Effect	Likelihood	Severity	Risk
Skin contact	Dryness and cracking	1	2	2

M3 _ M A D E

Contact with eyes	Irritation	2	2	3
Inhalation	<i>Long Effect</i>	1	4	4
Ingestion	<i>Irritation</i>	1	4	4
Risk rated: 1-4 = low, 5-8 = medium, 9-15 = high				
All hazards are adequately controlled with all control measures in place		☒ Yes – Proceed		
		☐ No – DO NOT PROCEED with the use of this substance		
Assessors Name Michele Di Nicola		Date 05/08/2026		

M3 _ M A D E

Date of Assessment:		05/08/2026	
SUBSTANCE			
Name of Substance:		MITREBOND ADHESIVE	
Supplier:		Unika Color Products Ltd	
Hazardous ingredients in the substance		ETHYL-2-CYANOACRYLATE	
Chemical Labelling			
(Check for symbol on the product data sheet or packaging)			
 	 	 	
☐ Toxic/ <i>Very Toxic</i>	☒ Harmful/Irritant	☐ Corrosive	☐ Long term health hazards such as cancer
 	 	 	 
☐ Explosive	☐ Oxidizing	☐ Flammable	☐ Tóxic to the environment
Does the substance react with any other substances?		Hazardous reactions will not occur under normal transport or storage conditions. Decomposition may occur on exposure to conditions or materials listed below: Materials to avoid: Strong oxidising agents. Strong acids. Haz. decomp. products: in combustion emits toxic fumes.	
WEL (Work Limit Exposure) of the product			
Risk Phrases Safety Phrases		WEL	
ETHYL-2-CYANOACRYLATE			
Workplace exposure limits:		Respirable dust	
State	8 hour TWA	15 min. STEL	8 hour TWA
UK	-	1.5 mg/m3	-
Substance hazard for health			
Body contact	Effect		
☒ Inhalation	Remove casualty from exposure ensuring one's own safety whilst doing so. Consult a doctor.		

M3 _ M A D E

☒ Ingestion	There may be soreness and redness of the mouth and throat.			
☒ Skin contact	There may be irritation and redness at the site of contact.			
☒ Eye contact	There may be irritation and redness. The eyes may water profusely.			
☐ Injected				
Health Warnings: Pneumonia may be the result if vomited material containing solvents reaches the lungs.				
FREQUENCY AND DURATION				
N/A				
WHO MIGHT BE HARMED				
Who is exposed to the substance	The operative			
Additional risks to certain groups or individuals	No			
What is the substance used for	Wardrobe installation and Kitchen installation			
Frequency of exposure	Daily			
CONTROL MEASURES				
EXISTING CONTROLS				
Design and use of appropriate work methods	Respiratory protection: Self-contained breathing apparatus must be available in case of emergency. Hand protection: Protective gloves. Eye protection: Safety glasses. Ensure eye bath is to hand. Skin protection: Protective clothing.			
ADDITIONAL CONTROLS				
Controls required for this substance	Engineering measures: Ensure there is sufficient ventilation of the area. Conditions to avoid: Heat. Humidity. Materials to avoid: Strong oxidising agents. Strong acids.			
PPE required when using the substance				
				
Eye Protection	Safety Gloves	Respiratory Protection	Ventilation	Other
✓	✓	✓	✓	✓
Safety goggles	Safety Gloves	Self-contained breathing apparatus must be available in case of emergency	Ensure there is sufficient ventilation of the area	Closed footwear
People using this substance have been provided with information or training on its use		☒ Yes ☐ No		
FIRST AID ACTION				
If contact with skin	Remove all contaminated clothes and footwear immediately unless stuck to skin. Wash immediately with plenty of soap and water			

M3 _ M A D E

If contact with eyes	Bathe the eye with running water for 15 minutes. Consult a doctor			
If inhaled	Remove casualty from exposure ensuring one's own safety whilst doing so. Consult a doctor.			
If swallowed	Wash out mouth with water. Consult a doctor			
Other				
OTHER PRECAUTIONS				
Storage	Store in a cool, well ventilated area. Keep container tightly closed.			
Spillage	Absorb into dry earth or sand. Transfer to a closable, labelled salvage container for disposal by an appropriate method.- Do not discharge into drains or rivers. Contain the spillage using bunding..			
Disposal	Transfer to a suitable container and arrange for collection by specialised disposal company. This product does not require a classification for transport.			
In case of a fire	Advice for fire-fighters: Wear self-contained breathing apparatus. Wear protective clothing to prevent contact with skin and eyes.			
Health Surveillance	Immediate effects can be expected after short-term exposure.			
RISK RATING FOLLOWING ADDITIONAL CONTROLS				
Hazards remaining	Effect	Likelihood	Severity	Risk
Skin contact	Dryness and cracking	1	2	2
Contact with eyes	Irritation	2	2	3
Inhalation	<i>Long Effect</i>	1	4	4
Ingestion	<i>Irritation</i>	1	4	4
Risk rated: 1-4 = low, 5-8 = medium, 9-15 = high				
All hazards are adequately controlled with all control measures in place		☒ Yes – Proceed ☐ No – DO NOT PROCEED with the use of this substance		
Assessors Name Michele Di Nicola		Date 05/08/2026		

M3 _ MADE

COSSH Statement Briefing Register

[illegible]

M3 _ MADE

[illegible]
